


UConn
2000

62

REPORT



UConn
UNIVERSITY OF CONNECTICUT

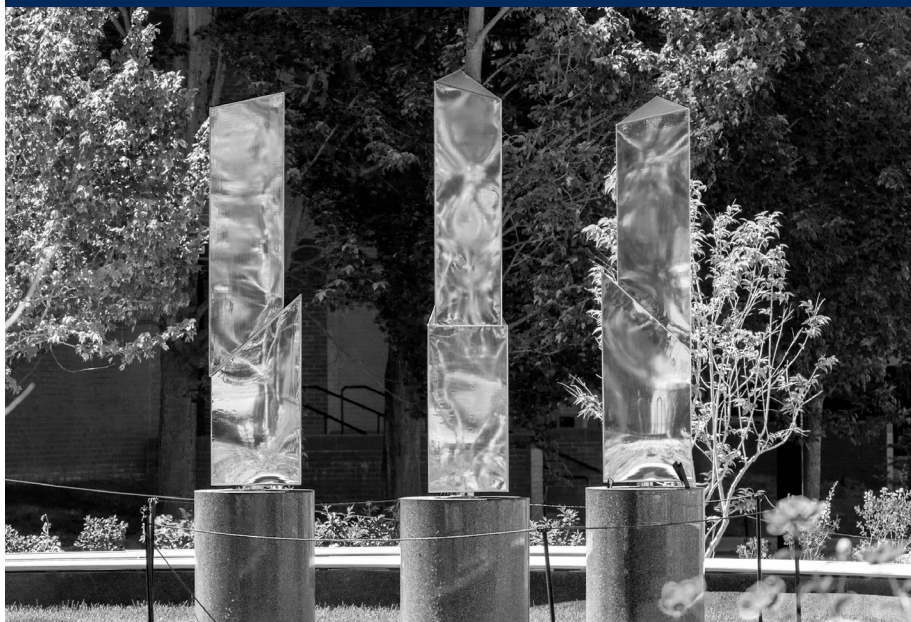

Thanks in good measure to UConn 2000, the University continues to attract scores of the state and nation's best and brightest students to Connecticut, most of whom live and work in the Nutmeg State after commencement.

UConn 2000

REBUILDING, RENEWING AND ENHANCING THE UNIVERSITY OF CONNECTICUT

July 2026

The Sixty Second
in a series of reports to

Governor Ned Lamont
and the
Connecticut General Assembly

UNIVERSITY OF CONNECTICUT

UCONN 2000: THE UPDATE

This is the sixty second in a series of semi-annual reports to the Governor and the General Assembly pursuant to the provisions of Sections 10a-109 through 10a-109y of the Connecticut General Statutes, originally An Act to Enhance the Infrastructure of the University of Connecticut, now known as UCONN 2000. These reports have been issued biannually since passage of UCONN 2000 on June 7, 1995. The law also requires a four-year progress report, which was filed on January 15, 1999, as well as two five-year performance reviews, which were submitted January 15, 2006 and January 15, 2011. The Act further provides that not later than December 31, 2019 and every 5 years thereafter, the University shall conduct an assessment of the University's progress in meeting the purposes set forth and incorporated in the Act by Next Generation Connecticut.

UCONN 2000: PROGRAM IMPROVEMENT

In 2008, the Construction Management Oversight Committee (CMOC) concluded its most significant and major undertaking, approving the policies and procedures developed by the University. In December 2014, the CMOC unanimously voted that the CMOC had successfully concluded its work as defined in statute and the four members appointed by the Governor and legislative leaders resigned from the committee. The committee has not been able to meet due to the lack of a quorum. The UConn Board of Trustees voted to transfer the CMOC's responsibilities to the Board's Buildings, Grounds and Environment Committee (BGE). BGE meets on a regular basis to review reports from the Office of Audit and Management Advisory Services (AMAS), which has taken on the statutory responsibilities of the Office of Construction Assurance. The office reviews the University's management of projects for conformance with the applicable policies and procedures governing construction, and is headed by the Chief Audit Executive, who reports to the Joint Audit & Compliance Committee, UConn Board of Trustees and the President. BGE also reviews the status of major projects and remaining code correction programs. In 2024, Public Act 24-22 was adopted which eliminated the CMOC and transferred its responsibilities to the UConn Board of Trustees, or one of the Board's committees, codifying what has been the practice, as noted above, since 2014.

Pursuant to Chapter 185b, Section 10a-109z of the Connecticut General Statutes (the Statute), the Board of Trustees for the University of Connecticut appointed the independent accounting firms of Marcum LLP (formerly UHY LLP), and RSM US LLP (formerly McGladrey LLP), to perform audits of the UCONN 2000 project expenditures for the Fiscal Years 2005 through 2010 and 2011 through 2015, respectively. With the exception of Fiscal Year 2013, Marcum and RSM issued an unmodified or clean audit opinion for each year of the engagement with no material weaknesses or significant deficiencies with internal controls. For Fiscal Year 2013, RSM identified a significant deficiency with an internal control related to the application of certain markups on change orders and base contracts. University management took steps to enhance the effectiveness of the internal control to ensure that markup calculations are accurate and in accordance with contract terms. CohnReznick was appointed to perform audits of the UCONN 2000 project expenditures for the Fiscal Years 2016 through 2020 and issued unmodified audit opinions with no material weakness or significant deficiencies with internal controls for each year of the engagement.

CBIZ CPAs, P.C. (formerly Mayer Hoffman McCann P.C.) has been appointed to perform audits of the UCONN 2000 project expenditures for the Fiscal Years 2021 through 2025. The Fiscal Year

2025 report contained no material weaknesses or significant deficiencies with internal controls as related to the statutory requirements.

The University employs building and life safety inspectors who review and sign off on all University construction plans and conduct field inspections to ensure that construction work meets all state building and life safety codes. The University inspectors work closely and effectively with the State Building Inspectors to ensure projects are code compliant.

RECENT CAPITAL FUNDING HISTORY: UNPARALLELED STATE COMMITMENT

In 2011, the State of Connecticut made strategic investments in the University of Connecticut and the University of Connecticut Health Center (UConn Health) to position Connecticut at the forefront of the growing bioscience industry. The investments were made with the promise that they would leverage other bioscience initiatives.

In 2011, the Bioscience Connecticut Initiative (Public Act 11-75), a bold \$864 million plan to reinvigorate all three areas of the UConn Health mission – research, education and clinical care was adopted. These investments aimed to generate long term sustainable economic growth based on bioscience research, innovation, entrepreneurship and commercialization. The project also called for short-term economic activity through a surge of construction-related jobs attributable to the expansion and renovation of infrastructure at UConn Health.

Construction components of Bioscience Connecticut on the UConn Health campus included:

- Renovating and modernizing, for the first time in its history, UConn Health’s original research facilities on the Farmington campus. This included expanding space for start-up bioscience businesses at the Cell and Genome Sciences Building.
- Constructing a new hospital tower.
- Renovating portions of the John Dempsey Hospital and the Clinic Building.
- Constructing, with private financing, a new UConn Health Outpatient Pavilion on the lower campus.
- Construction of an addition to the Academic Building to support an increase in Medical and Dental School class sizes.

Programmatic components of Bioscience Connecticut included:

- Recruiting new faculty, including clinicians and basic scientists, to increase healthcare access and federal and industry research awards.
- Doubling existing business incubator space to support commercialization and start-up companies.
- Expanding the School of Medicine and School of Dental Medicine class sizes by 30 percent.
- Implementing a loan forgiveness program for UConn Medical School graduates who pursue careers in primary care in Connecticut.

- Sponsoring a Health Disparities Institute to enhance research and the delivery of care to the minority and medically underserved populations of the state.
- Supporting the development of a primary care institute located on the campus of Saint Francis Hospital and Medical Center – the Connecticut Institute for Primary Care Innovation – intended to increase the number of primary care providers in the state.
- Supporting the development of a comprehensive cancer center to expand clinical trials and advance patient care at multiple sites in the Hartford region.

The groundbreaking for the first Bioscience Connecticut project took place on June 11, 2012. As previously reported, all projects associated with Bioscience Connecticut are complete and the UConn Health campus has been transformed into a modern, state-of-the-art academic medical center campus. Key construction projects that have been finalized include the Main Building Research Lab Renovations, the Technology Incubator Addition, the Academic Addition and Renovations, the Outpatient Pavilion, a new hospital bed tower known as the University Tower, three new parking garages, and many roadway improvements both on and off campus. The final project, Renovations to the Clinical Area of the Main Building, was completed in May 2019. With the completion of the final projects, FY18 was the last year of funding for UConn Health projects under the Bioscience Connecticut Initiative.

Also in 2011, legislation was enacted, which was subsequently amended in 2014 that provided \$169.5 million in funding to create the first building of a Technology Park (The Innovation Partnership Building – IPB) on the Storrs campus. The new Tech Park, like the Bioscience Connecticut Initiative, is a critical component of Connecticut’s plan to stimulate long-term economic growth by supporting innovation, new technologies and the creation of new companies and high-paying, sustainable jobs. Twenty-first century tech park models emphasize invention, incubation and entrepreneurship. The first building of the Tech Park will help hit the mark by promoting academic and industrial partnerships and by providing the physical and intellectual capacity to foster discovery. The IPB was completed in 2020.

In October 2011, just months after the passage of the capital investment at UConn Health, Public Act 11-2 was adopted and established the Connecticut Bioscience Collaboration Program (the “Collaboration”) supporting the establishment of a Bioscience cluster anchored by the world-renowned Jackson Laboratory. The Jackson Laboratory Center for Genomic Medicine research building, located on UConn Health’s campus in Farmington, opened in October 2014.

In July 2013, Public Act 13-233 was adopted and established Next Generation Connecticut for the purposes of construction, renovations, infrastructure and equipment related to the development of preeminence in the University of Connecticut's research and innovation programs. The Act not only authorized additional projects, but it also extended the capital program by 6 years through 2024 and added \$1.551 billion of additional funding. Pending annual operating appropriations, the Next Generation Connecticut initiative will also allow the University to (1) hire and support outstanding faculty, (2) train and educate more science, technology, engineering and math (STEM) graduates to meet the future workforce needs of Connecticut, and (3) initiate collaborative partnerships that lead to scientific and technological breakthroughs. During the 2017 legislative session, the phasing of the capital program funding was changed, and the Next Generation Connecticut initiative was extended by three years to 2027.

During 2024, Public Act 24-151 was adopted, which extends the NextGenCT program by four additional years to 2031 and increases project funding by \$625 million. This critical funding, along with a \$100 million philanthropy target, will be used to update STEM infrastructure to meet workforce needs, help address deferred maintenance needs, renovate portions of Gampel Pavilion for our national championship basketball programs, and upgrade the Field House and other athletic facilities to address Title IX inequities as follows.

UCONN 2000 Capital Extension (\$M)	
Life Sciences Building (aka Science 2)	\$269.5
Torrey Demo	25.0
Gant-Code Repairs & Renovations	100.0
Deferred Maintenance	50.0
Return Hydrogen Hub Funds	12.0
Gampel Renovations	100.0
Field House Renovation (Title IX + DM)	60.0
Coventry Boathouse (Title IX)	0.8
Freitas Renovation (Title IX)	7.0
Tennis Facility (Title IX)	0.7
Total UCONN 2000 Capital Extension	\$625.0

For UConn Health, during the 2021 legislative session, the General Assembly approved an additional \$25 million in the UCONN 2000 Program, Phase III, for deferred maintenance. Since this time, the State has authorized a limited amount of State General Obligation bond funding, outside of the UCONN 2000 program, to address deferred maintenance, equipment and information technology needs at UConn Health.

During 2025, Public Act 25-174 was adopted, which increased the UCONN 2000 program by \$4,000,000 to support the Gampel Pavilion Renovations project.

Also in 2025, Public Act 25-2 was adopted, which authorized the University of Connecticut Health Center Joint Venture Initiative. Under this initiative, UConn Health may establish subsidiaries or joint venture arrangements with the State to acquire, operate, improve, and, if necessary, divest hospital systems and related healthcare facilities in Connecticut. The legislation increases the UCONN 2000 bonding authorization by up to \$390 million over five fiscal years. Bond proceeds may be used for hospital acquisitions, capital improvements, deferred maintenance, information technology systems, and other costs related to the operation and integration of affiliated healthcare facilities. Entities formed pursuant to the joint venture initiative are not considered state agencies, and employees of such entities are not state employees. The initiative is intended to support the continued operation and financial stability of participating healthcare facilities and to further the clinical, educational, and research missions of UConn Health.

During 2026, Public Act 26-68 was adopted, increasing the UCONN 2000 bonding authorization by \$250.1 million over five fiscal years. The university will use these funds to support information technology equipment, and implementation of the Action Plan for Membership in the Association of American Universities (AAU), enabling UConn to recruit 10 Top-Tier research faculty.

In addition, \$180.1 million in previously authorized bond funding was incorporated into the UCONN 2000 program, and an additional \$40 million was authorized for the Field House and Gampel Pavilion projects. The transferred authorizations include:

- \$46.1 million for laboratory renovations and equipment to recruit Eminent Faculty Hires with demonstrated success in commercializing research and creating new businesses;
- \$3 million for digital learning infrastructure improvements at a regional campus;
- \$6 million for UConn Health telecommunications infrastructure upgrades and expansions;
- \$35 million for UConn Health equipment, library collections and telecommunications; and
- \$90 million for UConn Health deferred maintenance, code compliance and infrastructure improvements.

The resulting adjustments to the capital budget are summarized below:

Capital Funds (\$M)		Prior Approved State Bonds	New UConn 2000 Bonds	Total UConn 2000 Bonds
UConn				
	Information Technology Security & Equipment		\$10.0	\$10.0
	Digital Learning Infrastructure-Regional Campuses	3.0		3.0
	Top Tier Faculty: Start Up		20.0	20.0
	Eminent Faculty: Start Up	46.1		46.1
	Athletics Field House and Gampel Improvements		40.0	40.0
UConn Total		\$49.1	\$70.0	\$119.1
UConn Health				
	Clinical Equipment to Enhance Revenue Growth	35.0		35.0
	Deferred Maintenance	90.0		90.0
	Information Technology Security, Infrastructure & Equipment	6.0		6.0
UConn Health Total		\$131.0		\$131.0
Grand Total		\$180.1	\$70.0	\$250.1

UConn 2000: STATUS REPORT

MASTER PLANNING, DESIGN AND MANAGEMENT

The University's Master Plan provides a template for the development of the University's physical plant and infrastructure. The 1998 Storrs Campus Master Plan was updated in 2006 to reflect the extensive physical changes on all the campuses resulting from the UCONN 2000 initiatives. It should be noted that the Master Plan has been modified throughout the project planning, design and construction process of UCONN 2000. As part of the Technology Park initiative, an update to the North Campus Master Plan was prepared to delineate various site, vehicular and pedestrian pathways,

utility corridors, and landscape improvements to facilitate the future development of that part of campus. This work is incorporated in the comprehensive 2015 Master Plan for the campus.

The 2015 Master Plan reflects the impacts of the proposed projects included in the Next Generation Connecticut initiative and guides the development of the Storrs campus for the twenty (20) year period between 2015 and 2035. The 2015 Master Plan documents the state of existing conditions on campus and issues related to land use; space needs for academic, research, student life and administrative uses; recommended deferred maintenance and capital investments in the physical plant; environmental issues and sustainable design principles for future development; parking, circulation and transportation issues; and specific strategies to improve landscape quality and open spaces. The Master Plan references the programmatic ties to the Regional campuses, but does not include separate master plans for those locations.

The 2015 Master Plan is a comprehensive summary of the current conditions of the campus as of 2015 and a guideline for the proposed development of the Storrs campus over the next 20 years. The first ten years of development (2015-2024) are driven by the adopted Academic Vision Plan and fueled by the Next Generation Connecticut funding program. The plan also forecasts development that may occur beyond the Next Generation Connecticut projects (2028 -2035). This potential future development will require new funding sources and builds on the success of the first decade of growth. The total amount of development portrayed in the plan includes facilities that would be needed to grow the undergraduate student population by 5,000, accommodate a substantially larger research enterprise, repair or replace obsolete facilities and meet the commitments of the Climate Action Plan for a sustainable campus.

Implementation of the Master Plan

Future planned development will be programmed and designed to conform to the concepts and the development pattern contained in the Master Plan documents. The Master Plan will inform the design and implementation of the utility infrastructure, storm water management systems, roads and parking areas, landscape and land use, and individual projects. The urban form of the campus will take shape as envisioned in the Master Plan and will be refined by future design initiatives as specific developments are designed and built. While the Master Plan will inform and guide future development decisions, the final location, design, and programming of specific projects will be decided when those projects are implemented. Individual construction projects undertaken as part of this plan will, as always, be brought to the Board of Trustees for approval, along with the project budgets.

The final version of the Master Plan and its Executive Summary, Design Guidelines and Appendices, dated May 2015, were issued and are posted on the UConn website at <http://masterplan.uconn.edu/documents/>.

BIOSCIENCE CONNECTICUT

All of the Bioscience Connecticut construction projects are complete. Through March 2019, over 6,200 construction workers were employed on the Bioscience Connecticut projects and 85% of the construction contracts were awarded to Connecticut companies. The Minority / Women /

Disadvantaged Business participation reached 23%, exceeding the statutory minimum of 6.25% by nearly 17%.

The Bioscience Connecticut initiative planned for \$69 million in funding from operations, special eligible gifts or other sources toward new construction and renovation projects. UConn Health and the University of Connecticut Foundation have met this requirement.

CAPITAL PROGRAM

The Board of Trustees, at its June 17, 2026 meeting, approved the FY27 Capital Budget for UConn, Storrs and Regional Campuses, totaling \$475,000,000. This amount reflects \$442,100,000 of UCONN 2000 State bond funds, \$1,800,000 of gift funds, and \$31,100,000 of University funds.

Storrs & Regional Campuses

The following is a brief description of some of the named projects included in the FY27 Capital Budget or previous budgets, which are currently in planning, design or construction.

Academic and Research Facilities

The 285,000 gross square foot Gant Science Complex will be renovated to accommodate current and future University needs in response to growing student enrollment in STEM programs. These improvements will include classrooms, lecture halls, teaching and research laboratories, faculty offices and support spaces. Exterior site and plaza areas will be improved to make them more inviting and accessible to the campus community. The building envelope (façades and roofs) will be reconstructed to provide a more attractive waterproof skin with better energy performance. A new light court was built as part of phase 1 which enclosed the existing opening at the Gant Plaza. Phased construction began in Winter 2018. Phases 1 and 2 were completed in 2022. The work on Phase 3- North Wing commenced July 2025 and is anticipated to be completed by late Fall 2027.



New School of Nursing Building

The School of Nursing currently resides in Storrs Hall, a historic building constructed in 1906. In 2012, an expansion was added to accommodate the growing needs of the school, resulting in a total of 51,000 gross square feet (GSF). However, due to the continued growth of the school's program, the existing building can no longer adequately fulfill the school's requirements in terms of size and spatial configuration.

The goal of this project is to construct a new building for the Elisabeth DeLuca School of Nursing to accommodate an increased enrollment and to address the shortage of nurses, the changing nature of health care, and the increasing disparity in health outcomes. This project is being funded partially with a donation from the DeLuca Foundation, which will also support programming and operations. The new approximately 90,000 square foot building will be strategically located near the existing Brain Imaging Research Center, aligning with the vision outlined in the 2015-2035 Campus Master Plan.



Construction is underway with completion anticipated in January 2027.

Deferred Maintenance/Code Compliance/ADA Compliance/Infrastructure Improvements & Renovation Lump Sum and Utility, Administrative and Support Facilities

Per statute, the “deferred maintenance” portion of the project name is defined as “repair of an infrastructure or structure that was not maintained, repaired or replaced in the usual course of maintenance and repair.” In addition, the University intentionally designs projects to repair under-maintained facilities and infrastructure up to current standards and with necessary improvements to accommodate the current needs of the campuses. Also, the statutory named line clarification and new definition allows the University to construct new utility, infrastructure, administrative and support facilities as needed. In general, projects fall into one or more of the following categories:

- Safety, code and ADA required improvements
- Roof and exterior repairs
- Building mechanical system improvements
- Utilities repairs and upgrades
- General building renovations
- Roads, walks and grounds
- Environmental remediation
- New utility, infrastructure, administrative and support facilities

Some of the major projects to be funded within this category during FY27 are Gampel Pavilion Renovation, Field House, Environmental Remediation-Underground Storage Tank Relocations, Main

Campus Parking Development, and various programmatic renovations. Several of the projects recently completed or currently underway in this category are summarized below.

Boiler Plant Equipment Replacement & Utility Tunnel Connection

This project replaced the existing 1960's vintage Central Utility Plant (CUP) Boilers as well as completed the utility tunnel interconnection between the future Supplemental Utility Plant (SUP) and the existing Central Utility Plant. The new efficient boilers will reduce greenhouse gas emissions by 3.5%-5.25% from current levels.



The Boiler Plant Equipment Replacement and Utility Tunnel Connection project was implemented in three phases. In Phase I, the University pre-purchased three factory-fabricated, dual-fuel water-tube boilers.

In Phase II, the existing boilers were decommissioned and demolished in preparation for Phase III. Also, in phase II, the utility tunnel connection was completed. Work included extension of the steam, chilled water, and electrical connections from their current locations within the existing "North Utility Tunnel" at the northeast corner of the UTEB building into the CUP.

Phase III installed the new boilers in the CUP as well as the Supplemental Utility Plant. Work on the steam system will continue into Fall 2026.

Field House Renovation

The Greer Field House was the former Student Recreation Center, and upon their move to the new facility in August 2019, space became available to meet other Athletic Department program needs. In the summer of 2021, design consultants were hired to begin the programming and conceptual design for the backfill of the facility. The newly renovated spaces will be known as the Bailey Student-Athlete Success Center in recognition of alumnae Dr. Trisha M. Bailey whose significant gift has enabled the University to move forward with the project.

This project will bring athletics, research, sports medicine, hydrotherapy, training, rehabilitation, recovery, nutrition, compliance, clinical operations as well as academic support together in one building. The proposed program for the facility includes the establishment of the Nayden Center for Academic Excellence made possible from a generous gift from Denis and Britta Nayden. The Nayden Center will become the home for holistic development, academic accomplishment, and well-being for every student-athlete at UConn. This project also seeks to address Title IX requirements for the various athletic teams.

This project will renovate existing offices, support spaces, team rooms, coaches and officials' locker rooms, and team locker rooms for the following sports: men's and women's track and field, women's field hockey, women's rowing, women's tennis, and women's swimming & diving. These renovated spaces within the Field House and Wolff-Zackin facility will be constructed to a standard established in the new locker rooms within the Rizza Performance Center. Construction of the project began spring 2025 with scheduled completion in Winter 2027.



South Campus Infrastructure


In 2015, the University completed the NextGenCT Campus Masterplan and in 2016 the University performed a Framework Utility Analysis to create a systematic approach for infrastructure projects that support development of the NextGenCT program. The intent of this project is to provide infrastructure improvements in the South Campus district to support the construction and sustainable operation of the new South Campus Residence Hall.



The overall scope of this project will provide renewable infrastructure to the new South Campus Residence Hall and includes new utilities (steam, electric, hot and chilled water), communications, sanitary, stormwater, and domestic water for the South Campus Residence Hall, (CT Hall) and expansion of the South Campus Chiller Plant to accommodate a new geothermal heating and cooling system and to meet the needs of the Residence Hall and surrounding buildings. This project also makes utility connections that support the construction of the new School of Nursing project. Construction is complete with commissioning extending through fall 2026.

Innovation Partnership Building (IPB) Renovations for the Center for Clean Energy Engineering (C2E2)

The Innovation Partnership Building is UConn's premier center for cutting edge research and industry collaboration and innovation. This project will allow for increased synergy and research productivity by relocating the Center for Clean Energy Engineering (C2E2) from Depot Campus to the building. The project will be conducted in two phases, first the customization of existing offices and labs followed by the build-out of shell space. The project is now complete.

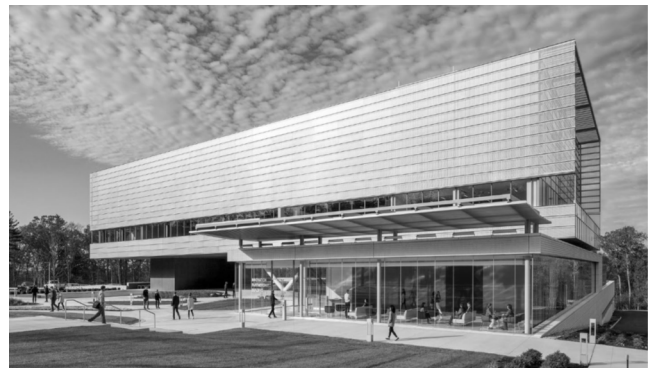

Mirror Lake Improvements

Mirror Lake has been a beloved and historic campus landmark since 1922. After multiple decades of deferred maintenance and campus growth within its watershed, numerous studies through 2021 concluded that critical improvements to the lake and its dam are necessary. Permitting, design, and preconstruction activities were completed in late 2022 however, a reduction and phasing of the scope of work became necessary due to budget constraints. The University then conducted collaborative working meetings with CT DEEP through early 2023, concluding with an amended Memorandum of Understanding for Mirror Lake and its watershed that attenuates stormwater flows from development since 1993.




The first phase of work focused on critical improvements and repairs to the dam, and a future phase will address stormwater attenuation and water quality improvements associated with construction in the watershed. The project is substantially complete.

Jones Annex Renovation

Faculty and professional staff in the department of Plant Science and Landscape Architecture support several outreach educational and fee-based services. Two of the most impactful programs include (1) a group of programs and services associated with the UConn Soil Nutrient Analysis Lab (SNAL), the Faculty Home & Garden Education Center (H&GEC), the Plant Diagnostic Center, the Turfgrass Diagnostic Service, the UConn Master Composter Program, and (2) the Integrated Pest Management (IPM) program. Presently, the H&GEC and the diagnostic services are located on the Storrs campus in the Ratcliffe-Hicks building while the SNAL is located on the Depot campus (Union Cottage).



This project renovates the existing Jones Annex building to create the George Leigh Minor Plant and Soil Health Center which consolidates the programs on Storrs campus to facilitate efficient management of personnel, collaboration between groups, and increase opportunities for professional staff to contribute to undergraduate life transformative educational activities, and other departmental service and professional improvement activities. Construction is complete.

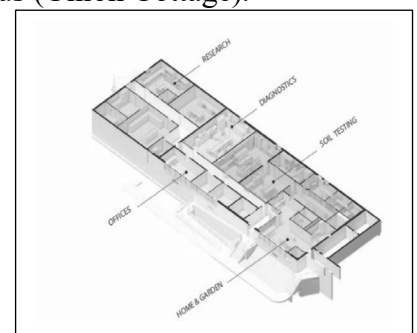


Pharmacy-Biology Building Research Support Expansion

The University's Animal Care facility must evolve to accommodate the growing research requirements of both current and incoming faculty, while also enhancing its support to the University community. This project renovates nearly 5,000 gsf of existing "shell space" within the Pharmacy-Biology building to facilitate the expansion and better support the operations of the adjacent animal care facility. The renovations will play a critical role in enhancing UConn's

competitiveness in grant competitions. Construction is underway and is expected to be complete in late fall 2026.

University Second Electrical Feed


The UConn Storrs campus receives electrical power from two sources: 1) the generation of power on campus at the Central Utility Plant by UConn owned and operated electrical generating turbines, and 2) the Utility provider's (Eversource) overhead power lines via a utility substation located west of the area "F" parking lot on the north side of North Eagleville Road. Each of the sources was originally designed with the capacity to independently provide all electricity needed for the campus, thus providing the University with the reliability and redundancy necessary should one or the other service be interrupted. Studies have shown that as the University continues to expand in accordance with its Master Plan, the electrical demand has increased to a point where both imported, and campus-based production of electrical power will need to be increased to maintain the required reliability and resiliency of the on-campus electrical distribution system.

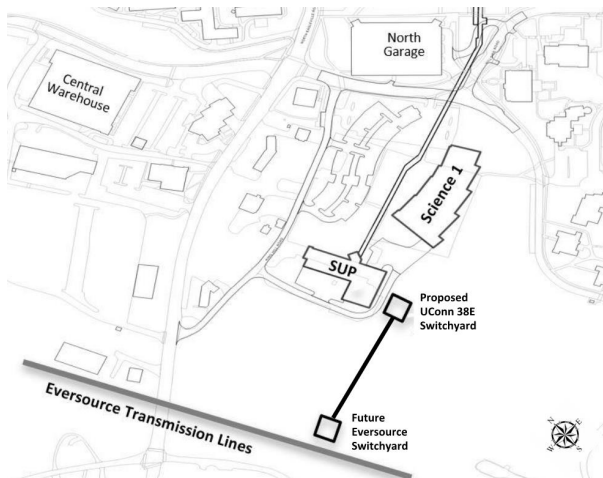

This project establishes a second connection to Eversource, terminating at a new 50-75 MVA transformer located on the exterior of the Supplemental Utility Plant in the substation switchgear yard. Included is a required modernization of the electrical distribution control system to manage multiple sources and the increased load demands which enables code compliant switching for personnel safety. Construction is expected to start in fall 2026. UConn and Eversource have executed an interconnection agreement for the new service.

Gampel Pavilion Renovation

The University is set to advance its efforts in upgrading Athletic Facilities by undertaking major renovations of the Harry A. Gampel Pavilion on the Storrs Campus, with the goal of modernizing the venue and creating more revenue-generating features and, as a prominent University landmark, Gampel Pavilion is the home of the men's and women's basketball teams and the men's golf team. The facility opened in January of 1990 and totals more than 171,000 square feet in the domed area. In the summer of 1996, its original seating capacity of 8,241 was increased by adding seats above each of the four entrance quadrants. The new 'sellout crowd' for UConn Basketball is approximately 10,000, making it the largest capacity on-campus basketball arena in New England.

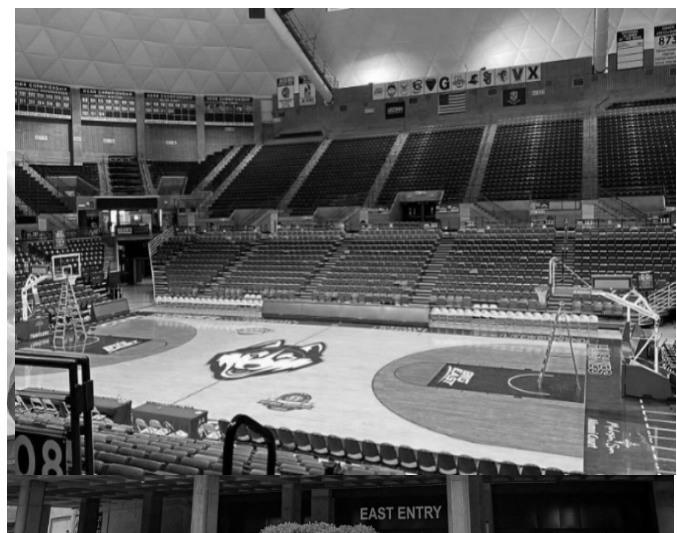

Phase 1 of the project focused on upgrading Wi-Fi equipment and services and installing structural components for new seating; this phase was completed in Fall 2025. Phase 2 will reconfigure the concourse to enhance circulation and expand concession areas, while adding premium fan amenities to increase overall revenue. The project also includes upgrades and consolidation of the athletic facilities and the Kinesiology Department. Additional improvements involve roof repairs and expanding the building footprint by enclosing the North Canopy. A new elevator will provide access to all levels. Construction on the remaining renovation elements began in Spring 2026.

Equipment, Library Collections & Telecommunications

The enhancement of the University's infrastructure includes its instructional and scientific equipment. The equipment replacement category permits the University to replace outmoded items with state-of-the-art laboratory devices and computers. The funding encompasses seven major categories: management information systems, computers, research equipment, instructional equipment, furnishings, operational and public safety support, and library materials.

UConn Health

In 2018, an external third party provided UConn Health with a ten-year Facilities Condition Assessment (FCA). The assessment identified \$646 million (inflation adjusted) in Deferred Maintenance needs across the following categories:

- **Recurring Deferred Renewal:** Items that have not been replaced during the normal course of maintenance that have reached or exceeded their expected life: \$323 million (e.g., original 1970 era HVAC systems).
- **Recurring Projected Renewal:** Items that during the 2026-2035 time period will "age out" and need to be replaced: \$273 million (e.g., roofs that are 25 years old now but will reach their 30-year life expectancy in the next 5 years and need to be replaced).
- **Nonrecurring:** Items that require replacement on a one-time basis: \$50 million (e.g., stair railings that are not code-compliant and need to be replaced but are not expected to be replaced again).

In addition to UCONN 2000 support, UConn Health has received State GO bond funding to support information technology, equipment, and deferred maintenance needs across its campus. These resources have been essential in addressing aging infrastructure, advancing technology and security upgrades, and replacing critical clinical and operational equipment. UConn Health will continue to seek additional capital funding on an ongoing basis to address the needs identified in the FCA.

Deferred Maintenance/Code Compliance/ADA Compliance/Infrastructure Improvements & Renovation Lump Sum and Utility, Administrative and Support Facilities

Per statute, the "deferred maintenance" portion of the project name is defined as "repair of an infrastructure or structure that was not maintained, repaired or replaced in the usual course of maintenance and repair." In addition, the University intentionally designs projects to repair under-maintained facilities and infrastructure up to current standards and with necessary improvements to accommodate the current needs of the campuses. The statutory named line clarification and new

definition also allows the University to construct new utility, infrastructure, administrative and support facilities as needed. In general, projects fall into one or more of the following categories:

- Safety, code and ADA required improvements
- Roof and exterior repairs
- Building mechanical system improvements
- Utilities repairs and upgrades
- General building renovations
- Roads, walks and grounds
- Environmental remediation
- New utility, infrastructure, administrative and support facilities

Numerous projects involving paving, roof replacements, academic and research renovations, and replacement of building infrastructure components are under design or construction including the IT Critical Equipment Redundancy Room, Central Sterile Processing Renovation, Interventional Radiology Renovation, Lab Medicine Renovation, and the Connecticut Tower Infrastructure Upgrade.

UCONN 2000: SET-ASIDE CONTRACTOR

Public Act 99-241 called for, among other things, information regarding use of Connecticut owned businesses on UCONN 2000 program projects, including those owned by women and minorities (“set-aside” contractors). Since Fiscal Year 1996, construction and related contracts for the UCONN 2000 program totaled \$5.5 billion from all fund sources; \$4.2 billion is strictly UCONN 2000 funds. As of June 2026, Connecticut businesses have accounted for \$3.0 billion of the total contracted dollars with “set-aside” general contractors and subcontractors accounting for \$1.0 billion. Overall, small business participation has amounted to \$593 million, minority business participation has amounted to \$142.3 million, and women-owned business participation has amounted to \$328.7 million.

UCONN 2000: FINANCE

Pursuant to Section 10a-109x of the Connecticut General Statutes, the semi-annual report to the General Assembly is to provide, among other things, information on the number of projects and securities authorized, approved and issued; the payment of debt service requirements, and the payment of principal and interest on the UCONN 2000 securities; and the amount of investment earnings. This section provides that information.

Legislative Authorizations - Selected Discussion

In May 2026, the General Assembly enacted, and the Governor signed Public Act 26-68 which increased the statutory authorizations for the UCONN 2000 bonds secured by the State Debt Service Commitment by \$250,100,000, in Fiscal Year 2027, for a total of \$5,565,000,000.

During November 2025, the Governor signed Public Act 25-2, which authorized the University of Connecticut Health Center Joint Venture Initiative. This act increases the statutory authorizations for the UCONN 2000 bonds secured by the State Debt Service Commitment by \$390,000,000, for Fiscal Year 2026 to 2030, for a total of \$5,314,900,000.

During June 2025, the Governor signed Public Act 25-174, which increased the statutory authorizations for the UCONN 2000 bonds secured by the State Debt Service Commitment by \$4,000,000, in Fiscal Year 2026, for a total of \$4,924,900,000.

During June 2024, the Governor signed Public Act 24-151, which extends the UCONN 2000 program by four years to 2031; increases the statutory authorizations for the UCONN 2000 bonds secured by the State Debt Service Commitment by \$625,000,000 for a total of \$4,920,900,000; and provides that not later than June 30, 2031, the University or the Foundation shall raise UConn 2000 philanthropic commitments and gifts of \$100,000,000 according to cumulative target milestones for Fiscal Years 2025 to 2031.

In 2023, the General Assembly enacted, and the Governor signed Public Act 23-1 that decreased the amount of bonds secured by the Debt Service Commitment that may be issued for fiscal year 2025 and in the aggregate by \$12,000,000 which decreased the Fiscal Year 1996 to 2027 total Debt Service Commitment amounts to \$4,295,900,000.

During June 2021, the Governor signed Public Act 21-2 increasing the Debt Service Commitment amount for Fiscal Year 2022 by \$25,000,000 to \$215,500,000. The estimated costs in the act were also changed including increasing the project known as “Deferred Maintenance/Code Compliance/ADA Compliance/Infrastructure & Improvements Renovation Lump Sum and Utility, Administrative and Support Facilities - Health Center”.

During March 2020, Public Act 20-1 was approved which reallocated the authorized Debt Service Commitment debt funding paid for by the State among the Fiscal Years 2020 through 2027 but did not change the total Debt Service Commitment amount authorized for UCONN 2000 projects.

During October 2017, the General Assembly passed Public Act 17-2 and the Governor signed on October 31, 2017 “An Act Concerning the State Budget for the Biennium Ending June 30, 2019, Making Appropriations Therefore, Authorizing and Adjusting Bonds of the State And Implementing Provisions of the Budget” that which among other things, moved some of the authorized DSC bond funding from Fiscal Years 2018 through 2023 and added it to 2024, and the newly added Fiscal Years 2025, 2026 and 2027 (without changing total DSC funding); and changed the name of the UCONN 2000 project “Deferred Maintenance/Code Compliance/ADA Compliance/Infrastructure Improvements & Renovation Lump Sum” to “Deferred Maintenance/Code Compliance/ADA Compliance/Infrastructure Improvements & Renovation Lump Sum and Utility, Administrative and Support Facilities” and UConn Health’s UCONN 2000 named project formally known as “Deferred Maintenance/Code/ADA Renovation Sum — Health Center” to the new UCONN 2000 project name of “Deferred Maintenance/Code Compliance/ADA Compliance/Infrastructure & Improvements Renovation Lump Sum and Utility, Administrative and Support Facilities – Health Center”.

During the May 2016 Special Session, the General Assembly passed Public Act 16-4 effective July 1, 2016, which among other things changed the name of the UCONN 2000 project “Deferred Maintenance/Code/ADA Renovation Lump Sum” to “Deferred Maintenance/Code Compliance/ADA Compliance/Infrastructure Improvements & Renovation Lump Sum” and also shifted \$26,000,000 of Debt Service Commitment authorizations from Fiscal Year 2017 to Fiscal Year 2018.

During May 2014, Governor Malloy signed Public Act 14-98 which clarified that the language in the UCONN 2000 legislation limiting UCONN 2000 debt applied only to the debt service commitment debt that the State pays and the limit does not apply to UCONN 2000 Special Obligation Student Fee Revenue bonds and other types of UCONN 2000 debt which the University and not the State pays. Public Act 14-5 was also signed in May 2014 and eliminated certain UCONN 2000 Act language that limited leasing outside the Storrs Campus.

In July 2013, Governor Malloy signed Public Act 13-233, “An Act Concerning Next Generation Connecticut”, which extended the UCONN 2000 program another six years until Fiscal Year 2024; increased the statutory authorizations for the UCONN 2000 bonds secured by the State’s debt service commitment by \$1.551 billion for a total of \$4,282,900,000; changed certain Fiscal Year bond authorizations; added a new named project called “Academic and Research Facilities”; and also added the housing language to the “Stamford Campus Improvements/Housing” project.

In July 2011, Governor Malloy signed Public Act 11-75, “An Act Concerning the University of Connecticut Health Center”, the Bioscience Connecticut initiative, which increased the statutory authorizations for the UCONN 2000 bonds secured by the State’s debt service commitment by \$262,900,000 for a total of \$2,731,900,000; changed certain Fiscal Year bond authorizations; eliminated a prior provision relating to the \$100 million contribution of federal, private or other non-state money; and provided for funding to renovate research laboratory space and create additional business incubator space.

On August 25, 2011, the Governor signed Public Act 11-57 for creation of a world-class Technology Park on the Storrs Campus to serve as a cornerstone for a new Connecticut research triangle. The Technology Park is expected to generate hundreds of new jobs in Connecticut, encourage new business growth, and leverage millions of dollars in federal and private research funding. The Technology Park will link to UConn Health in Farmington, the Connecticut Bioscience Initiative to Yale University in New Haven and others. A total of \$169.5 million of State General Obligation bond funding has been authorized by the State Bond Commission for the Technology Park. On August 26, 2011, the State Bond Commission authorized the first \$18 million of State General Obligation bonding to begin planning and design. On April 26, 2013, the State Bond Commission authorized the release of \$20 million in State General Obligation bonding to cover the purchase of equipment. On May 11, 2015, the State Bond Commission authorized the release of \$131.5 million in State General Obligation bonding to fund the construction of the new facility.

During the October 2011 special session, the General Assembly adopted Public Act 11-2 which established the Connecticut Bioscience Collaboration Program (the “Collaboration”) and authorized \$290,685,000 of State General Obligation bonds to be issued over a ten-year period and to be deposited in the Connecticut Bioscience Collaboration Fund. The Collaboration will support the establishment of a bioscience cluster anchored by the Jackson Laboratory for Genomic Medicine located on UCH’s Farmington campus.

In Fiscal Year 2002, the General Assembly enacted, and the Governor signed into law Public Act 02-3, An Act Concerning 21st Century UConn. This act authorized additional projects for the University and UConn Health for Phase III of UCONN 2000. This act amended Public Act 95-230 and extended the UCONN 2000 financing program.

Public Act 95-230 enabled the University to borrow money in its own name for a special 10-year capital improvement program designed to modernize, rehabilitate, and expand the physical plant of the University. It authorized projects for Phases I and II of UCONN 2000, estimated to cost \$1,250 million, of which \$962 million was financed by bonds of the University secured by the State Debt Service Commitment; \$18 million was funded by State General Obligation Bonds; and the balance of \$270 million was financed by gifts, other revenue, or borrowing resources of the University, including Special Obligation Student Fee Revenue bonds.

General Obligation Bonds

Section 10a-109 of the Connecticut General Statutes empowers the University to issue General Obligation Bonds secured by the State's Debt Service Commitment ("DSC"). These bonds are referred to as "General Obligation Debt Service Commitment Bonds" or "GO-DSC Bonds" throughout the remainder of this report. These bonds are issued pursuant to the General Obligation Master Indenture of Trust, dated as of November 1, 1995, between the University of Connecticut, as Issuer, and Fleet National Bank of Connecticut as Trustee (now U.S. Bank Trust Company, National Association). The University's Board of Trustees on November 10, 1995, and the State Bond Commission on December 21, 1995, approved the Master Indenture of Trust. The Master Indenture was subsequently amended and approved by the University's Board of Trustees on September 26, 2003, and the State Bond Commission on December 19, 2003. The Board of Trustees and the Governor approve the subsequent Supplemental Indenture for each bond issue. The University and the Office of the State Treasurer, working in conjunction, manage the GO-DSC Bond sale process.

General Obligation Bond Issues Completed

As of June 30, 2026, there have been forty GO-DSC Bond issues for the UCONN 2000 program including twenty-six new money and fourteen refunding bond issues.

There have been twenty-six new money GO-DSC Bonds issues totaling \$4,110,622,147 in par value which, together with original issue premium, funded \$4,444,000,000.00 of UCONN 2000 projects. The remaining balance, together with accrued interest and net original issue premium, funded the costs of issuance including deposits to the State Treasurer pursuant to the indentures.

Pursuant to Section 10a-109g of the Connecticut General Statutes, the UCONN 2000 GO-DSC Bonds authorized, approved and issued to date are listed below:

GO-DSC Bonds Phase I, II & III

<u>Date of Issue</u>	<u>Par Amount</u>	<u>TIC (1)</u>	<u>Bond Issue</u>
February 21, 1996	\$83,929,714.85	4.94%	1996 Series A ⁽²⁾
April 24, 1997	124,392,431.65	5.48%	1997 Series A ⁽²⁾
June 24, 1998	99,520,000.00	4.78%	1998 Series A ⁽²⁾
April 8, 1999	79,735,000.00	4.46%	1999 Series A ⁽²⁾
March 29, 2000	130,850,000.00	5.42%	2000 Series A ⁽²⁾
April 11, 2001	100,000,000.00	4.54%	2001 Series A ⁽²⁾
April 18, 2002	100,000,000.00	4.74%	2002 Series A ⁽²⁾⁽³⁾
March 26, 2003	96,210,000.00	3.97%	2003 Series A ⁽²⁾⁽⁴⁾
January 22, 2004	97,845,000.00	3.76%	2004 Series A ⁽²⁾⁽⁵⁾
March 16, 2005	98,110,000.00	4.20%	2005 Series A ⁽²⁾⁽⁶⁾
March 15, 2006	77,145,000.00	4.20%	2006 Series A ⁽²⁾⁽⁷⁾
April 12, 2007	89,355,000.00	4.14%	2007 Series A ⁽²⁾⁽⁸⁾
April 16, 2009	144,855,000.00	4.01%	2009 Series A ⁽²⁾⁽⁹⁾
May 25, 2010	97,115,000.00	3.64%	2010 Series A ⁽²⁾⁽¹⁰⁾
December 8, 2011	179,730,000.00	3.31%	2011 Series A ⁽²⁾⁽¹¹⁾
July 31, 2013	172,660,000.00	3.58%	2013 Series A ⁽²⁾⁽¹²⁾
April 22, 2014	109,050,000.00	3.37%	2014 Series A ⁽²⁾⁽¹³⁾
April 16, 2015	220,165,000.00	3.09%	2015 Series A ⁽²⁾⁽¹⁴⁾
April 21, 2016	261,510,000.00	2.76%	2016 Series A ⁽²⁾⁽¹⁵⁾
January 19, 2017	311,200,000.00	3.42%	2017 Series A ⁽¹⁶⁾
May 3, 2018	276,075,000.00	3.67%	2018 Series A ⁽¹⁷⁾
May 8, 2019	174,785,000.00	3.05%	2019 Series A ⁽¹⁸⁾
December 17, 2020	160,230,000.00	2.21%	2020 Series A ⁽¹⁹⁾
April 13, 2022	\$227,185,000.00	3.25%	2022 Series A ⁽²⁰⁾
November 21, 2023	\$224,540,000.00	4.12%	2023 Series A ⁽²¹⁾
March 24, 2026	\$226,115,000.00	3.60%	2026 Series A ⁽²²⁾
<u>March 24, 2026</u>	<u>\$148,315,000.00</u>	4.01%	2026 Bond Anticipation Notes ⁽²²⁾

Subtotal Phase I, II & III \$4,110,622,146.50

GO-DSC Refunding Bonds

January 29, 2004	\$216,950,000.00	3.55%	2004 Series A Refunding ⁽²⁾⁽⁵⁾
March 15, 2006	61,020,000.00	4.17%	2006 Series A Refunding ⁽²⁾⁽⁷⁾
April 12, 2007	46,030,000.00	4.22%	2007 Series A Refunding ⁽²⁾⁽⁸⁾
May 25, 2010	36,095,000.00	2.86%	2010 Series A Refunding ⁽²⁾⁽¹⁰⁾
December 8, 2011	31,905,000.00	2.29%	2011 Series A Refunding ⁽²⁾⁽¹¹⁾
July 31, 2013	51,250,000.00	2.71%	2013 Series A Refunding ⁽²⁾⁽¹²⁾
April 22, 2014	92,940,000.00	1.41%	2014 Series A Refunding ⁽²⁾⁽¹³⁾
April 16, 2015	34,625,000.00	2.15%	2015 Series A Refunding ⁽²⁾⁽¹⁴⁾
April 21, 2016	80,425,000.00	1.70%	2016 Series A Refunding ⁽¹⁵⁾
January 19, 2017	33,950,000.00	2.01%	2017 Series A Refunding ⁽²⁾⁽¹⁶⁾
May 8, 2019	64,680,000.00	2.23%	2019 Series A Refunding ⁽¹⁸⁾
December 17, 2020	\$119,085,000.00	0.95%	2020 Series A Refunding ⁽¹⁹⁾
November 21, 2023	\$133,505,000.00	3.57%	2023 Series A Refunding ⁽²¹⁾
<u>March 24, 2026</u>	<u>\$208,205,000.00</u>	2.70%	2026 Series A ⁽²²⁾

Subtotal Refunding Bonds \$1,210,665,000.00

- (1) TIC is the true interest cost reflecting the interest rate for the time value of money across an entire bond issue.
- (2) Bonds are no longer outstanding.
- (3) The GO-DSC 2002 Series A Bonds provided \$994,688.03 directly to the Office of the State Treasurer.
- (4) The GO-DSC 2003 Series A Bonds par amount of \$96,210,000 plus \$3,790,000 of the original issue premium totaled \$100,000,000 available for projects.
- (5) The GO-DSC 2004 Series A Bonds new money and GO-DSC Refunding 2004 Series A Bonds were issued under a single Official Statement with a par amount of \$216,950,000. The GO-DSC 2004 new money bonds totaled \$100,000,000 for projects, funded by the \$97,845,000 par amount plus \$2,155,000 of the original issue premium; and the GO-DSC Refunding 2004 Series A Bonds provided \$223,160,000 for a refunding escrow. Additional proceeds, including premium, funded the refunding escrow and the costs of issuance.
- (6) The GO-DSC 2005 Series A Bonds totaled \$100,000,000 available for projects funded by the \$98,110,000 par amount plus \$1,890,000 of the original issue premium. Phase II authorizations accounted for \$50 million and Phase III for \$50 million.
- (7) The GO-DSC 2006 Series A Bonds new money and GO-DSC Refunding 2006 Series A Bonds were issued under a single Official Statement with a par amount of \$138,165,000. The GO-DSC 2006 Series A Bonds new money totaled \$79,000,000 available for projects, funded by the \$77,145,000 par amount plus \$1,835,000 of the original issue premium, and the GO-DSC Refunding 2006 Series A Bonds provided \$65,472,900 for a refunding escrow. Additional proceeds, including premium, funded the refunding escrow and the costs of issuance.
- (8) The GO-DSC 2007 Series A Bonds new money and GO-DSC Refunding 2007 Series A Bonds were issued under a single Official Statement with a par amount of \$135,385,000. The GO-DSC 2007 Series A Bonds new money totaled \$89,000,000 available for projects, and the GO-DSC Refunding 2007 Series A Bonds provided \$49,505,476.89 for a refunding escrow. Additional proceeds, including premium, funded the refunding escrow and the costs of issuance.
- (9) The GO-DSC 2009 Series A Bonds par amount of \$144,855,000 plus \$5,145,000 of the original issue premium totaled \$150,000,000 available for projects.
- (10) The GO-DSC 2010 Series A Bonds new money and GO-DSC Refunding 2010 Series A Bonds were issued under a single Official Statement with a combined par amount of \$133,210,000. The GO-DSC 2010 Series A Bonds new money par amount of \$97,115,000 plus \$7,885,000 of the original issue premium totaled \$105,000,000 available for projects; and the GO-DSC Refunding 2010 Series A Bonds par amount of \$36,095,000 plus \$2,609,428.69 of the original issue premium provided \$38,704,428.69 for the refunding escrow. Additional proceeds, including premium, funded the costs of issuance.
- (11) The GO-DSC 2011 Series A Bonds new money and GO-DSC funding 2011 Series A Bonds were issued under a single Official Statement with a combined par amount of \$211,635,000. The GO-DSC 2011 Series A Bonds new money par amount of \$179,730,000 plus \$20,700,000 of the original issue premium totaled \$200,000,000 available for projects; and the GO-DSC Refunding 2011 Series A Bonds par amount of \$31,905,000 plus \$4,936,565.62 of the original issue premium provided 36,841,565.62 for the refunding escrow. Additional proceeds, including premium, funded the costs of issuance.
- (12) The GO-DSC 2013 Series A Bonds new money and GO-DSC Refunding 2013 Series A Bonds were issued under a single Official Statement with a combined par amount of \$223,910,000. The GO-DSC 2013 Series A Bonds new money par amount of \$172,660,000 plus \$16,340,000 of the original issue premium totaled \$189,000,000 available for projects; and the GO-DSC Refunding 2013 Series A Bonds par amount of \$51,250,000 plus \$6,978,911.08 of the original issue premium provided \$58,228,911.08 for the refunding escrow. Additional proceeds, including premium, funded the costs of issuance.
- (13) The GO-DSC 2014 Series A Bonds new money and GO-DSC Refunding 2014 Series A Bonds were issued under a single Official Statement with a combined par amount of \$201,990,000. The GO-DSC 2014 Series A Bonds new money par amount of \$109,050,000 plus \$10,950,000 of the original issue premium totaled \$120,000,000 available for projects; and the GO-DSC Refunding 2014 Series A Bonds par amount of \$92,940,000 plus \$6,573,683.06 of the original issue

premium provided \$99,513,683.06 for the refunding escrow. Additional proceeds, including premium, funded the costs of issuance.

- (14) The GO-DSC 2015 Series A Bonds new money and GO-DSC Refunding 2015 Series A Bonds were issued under a single Official Statement with a combined par amount of \$254,790,000. The GO-DSC 2015 Series A Bonds new money par amount of \$220,165,000 plus \$29,835,000 of the original issue premium totaled \$250,000,000 available for projects; and the GO-DSC Refunding 2015 Series A Bonds par amount of \$34,625,000 plus \$5,654,495.56 of the original issue premium totaled \$40,279,495.56 deposited to the refunding escrow. Additional proceeds, including premium, funded the costs of issuance.
- (15) The GO-DSC 2016 Series A Bonds new money and GO-DSC Refunding 2016 Series A Bonds were issued under a single Official Statement with a combined par amount of \$341,935,000. The GO-DSC 2016 Series A Bonds new money par amount of \$261,510,000 plus \$38,490,000 of the original issue premium totaled \$300,000,000 available for projects; and the GO-DSC Refunding 2016 Series A Bonds par amount of \$80,425,000 plus \$10,056,693.44 of the original issue premium totaled \$90,481,693.44 deposited to the refunding redemption fund and/or escrow. Additional proceeds, including premium, funded the costs of issuance.
- (16) The GO-DSC 2017 Series A Bonds new money and GO-DSC Refunding 2017 Series A Bonds were issued under a single Official Statement with a combined par amount of \$345,150,000. The GO-DSC 2017 Series A Bonds new money par amount of \$311,200,000 plus \$38,800,000 of the original issue premium totaled \$350,000,000 available for projects; and the GO-DSC Refunding 2017 Series A Bonds par amount of \$33,950,000 plus \$3,010,192.04 of the original issue premium totaled \$36,960,192.04 deposited to the refunding redemption fund and/or escrow. Additional proceeds, including premium, funded the costs of issuance.
- (17) The GO-DSC 2018 Series A Bonds were issued with a par amount of \$276,075,000 plus \$23,925,000 of the original issue premium funded \$300,000,000 for projects. Additional proceeds, including premium, funded the costs of issuance.
- (18) The GO-DSC 2019 Series A Bonds new money and GO-DSC Refunding 2019 Series A Bonds were issued under a single Official Statement with a combined par amount of \$239,465,000. The GO-DSC 2019 Series A Bonds new money par amount of \$174,785,000 plus \$25,215,000 of the original issue premium totaled \$200,000,000 available for projects; and the GO-DSC Refunding 2019 Series A Bonds par amount of \$64,680,000 plus \$8,133,086.38 of the original issue premium totaled \$72,813,086.38 deposited to the trustee bank redemption fund which was immediately used to call and refund all of the outstanding \$72,060,000 DSC 2009 bonds and pay the accrued interest on the same. Additional premium proceeds funded the costs of issuance.
- (19) The GO-DSC 2020 Series A Bonds new money and GO-DSC Refunding 2020 Series A Bonds were issued under a single Official Statement with a combined par amount of \$279,315,000. The GO-DSC 2020 Series A Bonds new money par amount of \$160,230,000 plus \$39,770,000 of the original issue premium funded \$200,000,000 for projects; and the GO-DSC Refunding 2020 Series A Bonds par amount of \$119,085,000 plus \$22,298,769.83 of the original issue premium totaled \$141,383,769.83 deposited to the trustee bank redemption fund and/or escrow. Additional premium proceeds funded the costs of issuance.
- (20) The GO-DSC 2022 Series A Bonds were issued with a par amount of \$227,185,000 plus \$32,815,000 of the original issue premium funded \$260,000,000 for projects. Additional premium proceeds funded the costs of issuance.
- (21) The GO-DSC 2023 Series A Bonds new money and GO-DSC Refunding 2023 Series A Bonds were issued under a single Official Statement with a combined par amount of \$358,045,000. The GO-DSC 2023 Series A Bonds new money par amount of \$224,540,000 plus \$15,460,000 of the original issue premium funded \$240,000,000 for projects; and the GO-DSC Refunding 2023 Series A Bonds par amount of \$133,505,000 plus \$8,825,161.01 of the original issue premium totaled \$142,330,161.01 deposited to the trustee bank redemption fund and/or escrow. Additional premium proceeds funded the costs of issuance.
- (22) The GO-DSC 2026 Series A Bonds included a new money component and a refunding component, and were issued under a single Official Statement along with the GO-DSC 2026 Bond Anticipation Notes, with a combined par amount of \$582,635,000.00. The GO-DSC 2026 Series A Bonds, new money component, par amount of \$226,115,000 plus \$27,031,161 of the original issue premium and the GO-DSC 2026 Bond Anticipation Notes, par amount \$148,315,000, funded \$400,000,000 for projects; and the GO-DSC 2026 Series A Bonds, refunding component, par amount of

\$208,205,000 plus \$23,348,524.25 of the original issue premium totaled \$231,533,524.25 deposited to the trustee bank escrow fund. Additional premium proceeds funded the costs of issuance.

General Obligation Bonds – Projects

During Fiscal Year 2005, the University finished Phase I and Phase II and initiated Phase III of the UCONN 2000 project authorizations secured by the State's DSC. As of June 30, 2026, the UCONN 2000 act provides for a total of \$5,565,000,000 of UCONN 2000 bonds secured by the State's DSC. As of June 30, 2026, the following projects totaling \$4,626,900,000 have been authorized to receive GO-DSC Bond proceeds by both the Governor and the Board of Trustees. The total authorization does not include the Thirty-fourth Supplemental Indenture which is pending the Governor's approval as of June 30.

Phase I & II**Authorized**

Agricultural Biotechnology Facility Completion	\$3,000,000.00
Agricultural Biotechnology Facility	9,400,000.00
Alumni Quadrant Renovations	11,183,623.91
Avery Point Marine Science Research Center-Phase I	30,000,000.00
Avery Point Marine Science Research Center-Phase II	7,254,246.03
Avery Point Renovation	4,875,717.46
Benton State Art Museum Addition	700,000.00
Business School Renovation	7,958,470.42
Central Warehouse New	6,933,751.77
Chemistry Building	53,062,000.00
Deferred Maintenance & Renovation Lump Sum	40,798,259.65
Deferred Maintenance & Renovation Lump Sum Balance	117,386,096.72
East Campus North Renovations	7,382,604.53
Equipment, Library Collections & Telecommunications	60,500,000.00
Equipment, Library Collections & Telecommunications Completion	105,812,000.00
Gant Plaza Deck	7,287,174.10
Gentry Renovation	9,664,596.69
Grad Dorm Renovations	2,928,227.59
Heating Plant Upgrade	9,969,000.00
Hilltop Dormitory Renovations	8,176,528.89
Ice Rink Enclosure	3,280,000.00
International House Conversion/(a.k.a. Museum of Natural History)	886,134.00
Litchfield Agricultural Center-Phase I	1,000,000.00
Mansfield Apartments Renovation	2,071,000.00
Mansfield Training School Improvements	3,500,000.00
Monteith Renovation	444,348.00
Music Drama Addition *	7,400,000.00
North Campus Renovation	10,996,050.15
North Superblock Site & Utilities	7,668,000.00
Northwest Quadrant Renovation-Phase I	2,001,000.00
Northwest Quadrant Renovation-Phase II	30,000,000.00
Parking Garage-North	9,658,000.00
Pedestrian Walkways/(a.k.a. Fairfield Road Pedestrian Mall)	6,074,000.00
School of Business	25,652,366.00
School of Pharmacy	88,609,000.00
Shippee/Buckley Renovations	6,920,000.00
South Campus Complex	12,251,000.00
Stamford Downtown Relocation-Phase I	55,781,471.55
Student Union Addition	44,622,633.00
Technology Quadrant-Phase IA	39,993,000.00
Technology Quadrant-Phase II	34,120,000.00
Torrey Life Science Renovation	251,109.43
Towers Renovation	17,950,243.11

Underground Steam & Water Upgrade	6,000,000.00
Underground Steam & Water Upgrade Completion	6,000,000.00
Waring Building Conversion	11,452,000.00
Waterbury Property Purchase	200,000.00
West Campus Renovations	519,507.20
White Building Renovation	2,427,268.80
<u>Wilbur Cross Building Renovation</u>	<u>19,999,571.00</u>
TOTAL PHASE I & II PROJECTS	\$962,000,000.00

** Board of Trustees added Project 2/22/2001*

<u>Phase III - Storrs and Regional Campuses</u>	<u>Authorized</u>
Academic and Research Facilities	489,704,438.00
Arjona and Monteith (new classroom buildings)	128,219,870.93
Avery Point Campus Undergraduate and Library Building	10,461,245.77
Avery Point Renovation	8,327,447.54
Beach Hall Renovations	5,146,688.33
Benton State Art Museum Addition	2,903,508.88
Biobehavioral Complex Replacement	3,495,807.00
Bishop Renovation	2,480,140.83
Deferred Maintenance/Code Compliance/ADA Compliance/ Infrastructure Improvements & Renovation Lump Sum and Utility, Administrative and Support Facilities	1,065,493,262.83
Engineering Building (with Environmental Research Institute)	92,579,389.76
Equipment, Library Collections & Telecommunications	219,441,656.00
Family Studies (DRM) Renovation	2,868,306.20
Farm Buildings Repairs/Replacement	6,408,304.09
Fine Arts Phase II	38,792,721.25
Floriculture Greenhouse	6,691,798.67
Gant Building Renovations and New Life Sciences Building	12,455,770.32
Gentry Completion	9,628,208.95
Harry A. Gampel Pavilion and Hugh S. Greer Field House	-
Hartford Relocation Acquisition/Renovation	139,027,625.42
Heating Plant Upgrade	11,877,724.42
Intramural, Recreational and Intercollegiate Facilities	31,009,920.63
Jorgensen Renovation	3,899,128.58
Koons Hall Renovation/Addition	1,461,146.00
Lakeside Renovation	3,800,000.00
Law School Renovations/Improvements	16,660,677.09
Manchester Hall Renovation	772,577.13
Mansfield Training School Improvements	3,000,000.00
Natural History Museum Completion	500,000.00
North Hillside Road Completion	6,700,000.00
Old Central Warehouse *	126,000.00
Parking Garage #3	75,214.27
Psychology Building Renovation/Addition	24,337,399.00
Residential Life Facilities	248,538,476.01

School of Pharmacy/Biology Completion	6,000,000.00
Stamford Campus Improvements/Housing	1,500,870.00
Storrs Hall Addition	14,664,091.44
Student Union Addition	13,000,000.00
Support Facility (Architectural and Engineering Services)	16,583.05
Torrey Renovation Completion and Biology Expansion	1,530,373.00
Torrington Campus Improvements	369,156.42
Waterbury Downtown Campus	1,608,764.00
West Hartford Campus Renovations/Improvements	6,774,305.19
<u>Young Building Renovation/Addition</u>	<u>23,651,403.00</u>
Total – Storrs & Regionals Project List	\$2,666,000,000.00

UConn Health

CLAC Renovation Biosafety Level 3 Lab	\$15,901,465.91
Deferred Maintenance/Code Compliance/ADA Compliance/Infrastructure & Improvements Renovation Lump Sum and Utility, Administrative and Support Facilities - Health Center	76,959,697.17
Dental School Renovation	3,525,000.00
Equipment, Library Collections and Telecommunications - Health Center	116,429,390.00
Library/Student Computer Center Renovation	1,266,459.97
Main Building Renovation	117,484,315.91
Medical School Academic Building Renovation	39,578,232.00
Planning and Design Costs	25,000,000.00
Research Tower	67,992,229.21
Support Building Addition/Renovation	100,000.00
The University of Connecticut Health Center New Construction and Renovation	386,663,209.83
<u>The University of Connecticut Health Center Joint Venture Initiative</u>	<u>148,000,000.00</u>
Total – UConn Health Project List	\$998,900,000.00

TOTAL PHASE III PROJECTS

\$3,664,900,000.00

TOTAL GO-DSC BONDS: PHASE I, II AND III PROJECTS

\$4,626,900,000.00

* The Old Central Warehouse was added by PA 07-108 effective 7-1-2007

General Obligation Bonds – Refundings

Pursuant to Section 10a-109 of the Connecticut General Statutes, the University may issue refunding securities.

As of June 30, 2026, the University achieved \$125.0 million in cumulative gross debt service savings for Connecticut taxpayers by issuing GO-DSC Refunding Bonds in 2004, 2006, 2007, 2010, 2011, 2013, 2014, 2015, 2016, 2017, 2019, 2020, 2023 and 2026 as detailed below.

On January 29, 2004, the University achieved \$15.2 million in debt service savings for Connecticut taxpayers through the \$216,950,000 of UCONN 2000 GO-DSC Refunding 2004 Series A Bonds. Proceeds pre-refunded \$223,160,000 of the portions of the 1996, 1997, 1998, 2000, 2001 and 2002 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$15,215,582.84 on a gross cash debt service savings basis or \$10,117,718.77 on a net present value basis (4.53% savings over refunded bonds debt service) spread across Fiscal Years 2004 to 2020.

On March 15, 2006, the University achieved \$4.0 million in debt service savings through the issuance of \$61,020,000 of UCONN 2000 GO-DSC Refunding 2006 Series A Bonds. Proceeds pre-refunded \$61,675,000 of the portions of the 1998, 1999, 2000, 2001 and 2002 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$4,003,734.09 on a gross cash debt service savings basis or \$2,495,916.47 on a net present value basis (3.94% savings over refunded bonds debt service) spread across Fiscal Years 2006 to 2020.

On April 12, 2007, the University achieved \$1.7 million in debt service savings through the issuance of \$46,030,000 of UCONN 2000 GO-DSC Refunding 2007 Series A Bonds. Proceeds pre-refunded \$46,695,000 of the portions of the 2002 and 2003 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$1,680,056.23 on a gross cash debt service savings basis or \$1,387,269.87 on a net present value basis (2.97% savings over refunded bonds debt service) spread across Fiscal Years 2008 to 2022.

On May 25, 2010, the University achieved \$1.8 million in debt service savings through the issuance of \$36,095,000 of UCONN 2000 GO-DSC Refunding 2010 Series A Bonds. Proceeds pre-refunded \$35,885,000 of portions of the 1999, 2001, 2003 and 2004 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$1,791,739.17 on a gross cash debt service savings basis or \$1,470,720.91 on a net present value basis (4.1% savings over refunded bonds debt service) spread across Fiscal Years 2011 to 2021.

On December 8, 2011, the University achieved \$1.9 million in debt service savings through the issuance of \$31,905,000 of UCONN 2000 GO-DSC Refunding 2011 Series A Bonds. Proceeds pre-refunded \$33,735,000 of portions of the 2003 and 2004 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$1,918,938.89 on a gross cash debt service savings basis or \$1,680,287.49 on a net present value basis (5.0% savings over refunded bonds debt service) spread across Fiscal Years 2011 to 2021.

On July 31, 2013, the University achieved \$4.8 million in debt service savings through the issuance of \$51,250,000 of UCONN 2000 GO-DSC Refunding 2013 Series A Bonds. Proceeds pre-refunded \$54,375,000 of portions of the 2004 and 2005 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$4,768,953.75 on a gross cash debt service savings basis or \$3,982,216.07 on a net present value basis (7.3% savings over refunded bonds debt service) spread across Fiscal Years 2014 to 2024.

On April 22, 2014, the University achieved \$8.5 million in debt service savings through the issuance of \$92,940,000 of UCONN 2000 GO-DSC Refunding 2014 Series A Bonds. Proceeds refunded \$97,930,000 of portions of the 2004 and 2005 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$8,491,280.28 on a gross cash debt service savings basis or \$7,697,944.62 on a net present value basis (7.9% savings over refunded bonds debt service) spread across Fiscal Years 2015 to 2025.

On April 16, 2015, the University achieved \$4.9 million in debt service savings through the issuance of \$34,625,000 of UCONN 2000 GO-DSC Refunding 2015 Series A Bonds. Proceeds refunded \$38,550,000 of certain maturities of the 2006 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$4,944,870.51 on a gross cash debt service savings basis or \$4,281,359.73 on a net present value basis (11.1% savings over refunded bonds debt service) spread across Fiscal Years 2016 to 2026.

On April 21, 2016, the University achieved \$8.5 million in debt service savings through the issuance of \$80,425,000 of UCONN 2000 GO-DSC Refunding 2016 Series A Bonds. Proceeds refunded

\$46,535,000 of certain maturities of the 2006 UCONN 2000 GO-DSC Refunding Bonds and pre-refunded \$42,000,000 of certain maturities of the 2007 UCONN 2000 GO-DSC Bonds. Debt service savings amounted to \$8,489,980.00 on a gross cash debt service savings basis or \$7,751,484.82 on a net present value basis (8.8% savings over refunded bonds debt service) spread across Fiscal Years 2017 to 2027.

On January 19, 2017, the University achieved \$3.8 million in debt service savings through the issuance of \$33,950,000 of UCONN 2000 GO-DSC Refunding 2017 Series A Bonds. Proceeds refunded \$36,095,000 of the 2007 UCONN 2000 GO-DSC Refunding Bonds 2018 to 2022 maturities. Debt service savings amounted to \$3,763,591.11 on a gross cash debt service savings basis or \$3,295,890.33 on a net present value basis (9.1% savings over refunded bonds debt service) spread across Fiscal Years 2018 to 2022.

On May 8, 2019, the University achieved \$9.6 million in debt service savings through the issuance of \$64,680,000 of UCONN 2000 GO-DSC Refunding 2019 Series A Bonds. Proceeds refunded \$72,060,000 of the 2009 UCONN 2000 GO-DSC Refunding Bonds 2020 to 2029 maturities. Debt service savings amounted to \$9,567,690.89 on a gross cash debt service savings basis or \$8,110,020.66 on a net present value basis (10.9% over refunded bonds debt service) spread across Fiscal Years 2020 to 2029.

On December 17, 2020, the University achieved \$29.0 million in debt service savings through the issuance of \$119,085,000 (plus original issue premium) of UCONN 2000 GO-DSC Refunding 2020 Series A Bonds. Proceeds refunded \$138,340,000.00 of principal of outstanding bonds as follows: on December 17, 2020 to call and refund \$43,695,000.00 of certain maturities of the GO-DSC 2010 bonds principal outstanding plus \$724,583.42 of accrued interest for a total of \$44,419,583.42; and on February 15, 2021 to call and refund \$89,850,000.00 of the GO-DSC 2011 new money bonds principal outstanding plus \$2,208,875.00 accrued interest for a total of \$92,058,875.00; and to call and refund \$4,795,000.00 of the GO-DSC 2011 Refunding bonds Principal outstanding, plus \$119,875.00 of accrued interest for a total of \$4,914,875.00. Additional premium proceeds funded the costs of issuance. Apart from the 2/15/2021 maturity of the 2011 New Money and Refunding bonds all the outstanding principal was refunded. Debt service savings amounted to \$29,010,290.14 on a gross cash debt service savings basis or \$27,416,150.18 on a net present value basis (19.81% over refunded bonds debt service) spread across Fiscal Years 2021 to 2031.

On November 21, 2023, the University achieved \$10.8 million in debt service savings through the issuance of \$133,505,000 of UCONN 2000 GO-DSC Refunding 2023 Series A Bonds. Proceeds refunded \$86,315,000 of the 2013 UCONN 2000 GO-DSC Bonds 2024 to 2033 maturities and \$54,505,000 of the 2014 UCONN 2000 GO-DSC Bonds 2025 to 2034 maturities. Debt service savings amounted to \$10,838,391.67 on a gross cash debt service savings basis or \$8,434,775.58 on a net present value basis (5.99% over refunded bonds debt service) spread across Fiscal Years 2024 to 2034.

On March 24, 2026, the University achieved \$20.5 million in debt service savings through the issuance of \$208,205,000 of UCONN 2000 GO-DSC 2026 Series A Bonds, refunding component. Proceeds refunded \$99,065,000 of the 2015 UCONN 2000 GO-DSC Bonds 2027 to 2035 maturities and \$130,750,000 of the 2016 UCONN 2000 GO-DSC Bonds 2027 to 2036 maturities. Debt service savings amounted to \$20,533,327.08 on a gross cash debt service savings basis or \$17,362,362.03 on a net present value basis (7.41% over refunded bonds debt service) spread across Fiscal Years 2027 to 2036.

Special Obligation Student Fee Revenue Bonds

UCONN 2000 also authorizes the University to issue Special Obligation bonds. Unlike the UCONN 2000 GO-DSC Bonds that are paid from the State's General Fund, debt on the Special Obligation bonds is paid from certain pledged revenues of the University as defined in the particular bond series indenture.

A Special Capital Reserve Fund may be established for UCONN 2000 Special Obligation bond issues only if the Board of Trustees determines that the Special Obligation bond issue is self-sufficient as defined in the Act. The self-sufficiency finding by the University must be submitted to and confirmed as not unreasonable or arbitrary by the State Treasurer prior to issuance of the bonds. Once approved, the Special Capital Reserve Fund is funded at issuance by the University to meet the minimum capital reserve requirement.

Special Obligation Student Fee Revenue Bond Issues Completed

The UCONN 2000 Special Obligation Student Fee Revenue Bonds ("SO-SFR Bonds") authorized, approved and issued to date are listed below.

SO-SFR Bonds have been issued pursuant to the Special Obligation Indenture of Trust, dated as of January 1, 1997, between the University as Issuer and U.S. Bank Trust Company, National Association as successor to State Street Bank & Trust as Trustee ("the Special Obligation Master Indenture"). The Board of Trustees approved the Special Obligation Master Indenture on November 8, 1996. The Board of Trustees and the Governor approve the subsequent Supplemental Indentures for each Special Obligation bond issue.

There have been nine bond issues, including four refundings, pursuant to the Special Obligation Master Indenture that, as mentioned above, are not secured by the State's DSC. The University and the Office of the State Treasurer, working in conjunction, manage the Special Obligation bond sale process. UCONN 2000 SO-SFR Bonds issued to date are summarized below:

UCONN 2000 SO-SFR Bonds

<u>Date of Issue</u>	<u>Par Amount</u>	<u>TIC⁽¹⁾</u>	<u>Bond Issue</u>
February 4, 1998	\$33,560,000	5.08%	1998 Series A ⁽²⁾
June 1, 2000	\$89,570,000	6.02%	2000 Series A ⁽²⁾
February 14, 2002	\$75,430,000	4.94%	2002 Series A ⁽²⁾
March 29, 2018	\$141,725,000	4.06%	2018 Series A
November 21, 2023	\$97,140,000	5.00%	2023 Series A
February 27, 2002	\$96,130,000	4.89%	Refunding 2002 Series A ⁽²⁾
June 16, 2010	\$47,545,000	3.14%	Refunding 2010 Series A ⁽²⁾
December 13, 2012	\$87,980,000	2.47%	Refunding 2012 Series A ⁽²⁾
November 15, 2022	\$52,515,000	3.80%	Refunding 2022 Series A

⁽¹⁾ TIC is the true interest cost reflecting the interest rate for the time value of money across an entire bond issue. The UCONN 2000 SO-SFR Bonds are generally issued for an approximate 30-year final maturity, compared to a 20-year final maturity for the GO-DSC Bonds; hence the TIC may appear relatively higher for SO-SFR Bonds.

⁽²⁾ Bonds are no longer outstanding

On February 4, 1998, the University issued \$33,560,000 of UCONN 2000 Student Fee Revenue 1998 Series A Bonds with a final maturity of November 15, 2027. The Special Obligation First Supplemental Indenture was also dated January 1, 1997 and authorized the issuance of bonds up to a principal amount not to exceed \$30,000,000 for construction of the South Campus Residence and Dining Hall, plus amounts necessary to fund a Special Capital Reserve Fund (“SCRF”) and provide for costs of issuance. The University managed the issuance and sale of these bonds and realized a favorable true interest cost over the term. Debt service for these bonds is paid from pledged revenues as further defined in the Indenture of Trust. Such pledged revenues also help support future operation and maintenance costs for facilities built or renovated through UCONN 2000.

On June 1, 2000, the University issued \$89,570,000 of the UCONN 2000 Student Fee Revenue 2000 Series A Bonds pursuant to the Special Obligation Master Indenture and the SO-SFR Bonds Second Supplemental Indenture dated as of May 1, 2000. Bond proceeds funded \$87,000,000 of construction for the Hilltop Dormitory, Hilltop Student Rental Apartments, and Parking Garage South. They also provided for capitalized interest and costs of issuance. The \$89,570,000 Student Fee Revenue 2000 Series A Bonds were defeased in substance on February 27, 2002, as further described below, and are no longer reflected as outstanding debt on the University’s financial statements.

On February 14, 2002, the University issued \$75,430,000 of the UCONN 2000 Student Fee Revenue 2002 Series A Bonds pursuant to the Special Obligation Master Indenture and the SO- SFR Bonds Fourth Supplemental Indenture dated November 16, 2001. Bond proceeds funded \$72,180,000 of construction for the Alumni Quadrant Renovations, Shippee/Buckley Renovations, East Campus North Renovations, Towers Renovations (including Greek Housing), and North Campus Renovations (including North Campus Student Suites and Apartments).

On March 29, 2018, the University issued \$141,725,000 of the UCONN 2000 Student Fee Revenue 2018 Series A Bonds pursuant to the Special Obligation Master Indenture and the SO- SFR Bonds Fifth Supplemental Indenture dated as of November 21, 2017. Bond proceeds funded \$152,000,000 of construction for the UCONN 2000 Project Intramural, Recreational and Intercollegiate Facilities including a new Student Recreation Center, associated infrastructure, and Stadia. They also funded capitalized interest and costs of issuance.

On November 21, 2023, the University issued \$97,140,000 of the UCONN 2000 Student Fee Revenue 2023 Series A Bonds pursuant to the Special Obligation Master Indenture and the SO- SFR Bonds Sixth Supplemental Indenture dated as of November 1, 2023. Bond proceeds funded \$100,000,000 towards the design, construction, equipping and/or furnishing for the UCONN 2000 Project, Residential Life Facilities, for a new student residence hall located on South Campus in Storrs, plus costs of issuance.

Special Obligation Student Fee Revenue Bonds - Projects

As of June 30, 2026, the following eleven projects totaling \$441,180,000 have been authorized to receive SO-SFR Bond proceeds (some of these projects were also supported by GO-DSC or other funding) as follows:

<u>Phase I & II</u>	<u>Authorized & Issued</u>
Alumni Quadrant Renovations	7,000,000.00
East Campus North Renovations	1,000,000.00
Hilltop Dormitory New	21,000,000.00
Hilltop Student Rental Apartments	42,000,000.00
North Campus Renovation	45,000,000.00
(including North Campus Student Suites and Apartments)	
Parking Garage-South	24,000,000.00
Shippee/Buckley Renovations	5,000,000.00
South Campus Complex	30,000,000.00
Towers Renovations (including Greek Housing)	14,180,000.00
TOTAL SO-SFR BONDS: PHASE I AND II PROJECTS	<u>\$189,180,000.00</u>
 <u>Phase III</u>	
Intramural, Recreational and Intercollegiate Facilities	152,000,000.00
Residential Life Facilities	100,000,000.00
TOTAL SO-SFR BONDS: PHASE III PROJECTS	<u>\$252,000,000.00</u>
TOTAL SO-SFR BONDS AUTHORIZED & ISSUED	<u>\$441,180,000.00</u>

Special Obligation Student Fee Revenue Bonds – Refundings

Pursuant to Section 10a-109 of the Connecticut General Statutes, the University may issue refunding securities. The University achieved a total of \$50.3 million in gross debt service savings for Connecticut taxpayers by issuing SO-SFR Refunding Bonds or calling and retiring debt as follows.

On February 27, 2002, the University achieved debt service savings of \$3,553,672 on a gross cash debt service savings basis or \$2,383,106 on a net present value basis (3.036% savings over refunded bonds debt service) through its issuance of \$96,130,000 of the UCONN 2000 Student Fee Revenue Refunding 2002 Series A Bonds. The bonds were issued pursuant to the Special Obligation Master

Indenture and the SO-SFR Bonds Third Supplemental Indenture, dated as of February 1, 2002. Proceeds were used to take advantage of favorable market conditions to advance refund and defease in substance all the \$89,570,000 of Student Fee Revenue 2000 Series A Bonds outstanding. Proceeds were deposited with the Trustee bank in an irrevocable escrow fund sufficient to satisfy future debt service and call premiums on the prior issue.

On June 16, 2010, the University achieved debt service savings of \$9,479,927 on a gross cash debt service savings basis or \$7,211,753 on a net present value basis (9.915% savings over refunded bonds debt service) (including the free up of \$2,126,425 of SCRF amounts), through its issuance of \$47,545,000 of the UCONN 2000 Student Fee Revenue Refunding 2010 Series A Bonds. The bonds were issued pursuant to the Special Obligation Master Indenture and the SO-SFR Bonds Third Supplemental Indenture, dated as of February 1, 2002. Proceeds were used to take advantage of favorable market conditions to refund, advance refund and defease in substance \$51,305,000 of prior bonds (including \$25,140,000 of the Student Fee Revenue 1998 Series A Bonds and \$26,165,000 of the Student Fee Revenue 2002 Series A Bonds outstanding). The par amount of \$47,545,000 plus \$4,267,926 of the original issue premium and \$2,126,425 from the 1998 Special Capital Reserve Fund release were deposited with the Trustee bank in a \$53,939,351 irrevocable escrow fund to satisfy future debt service and call premiums on the prior issues.

On December 13, 2012 the University achieved debt service savings of \$31,861,283 on a gross cash debt service savings basis or \$26,701,079 on a net present value basis (25.2% savings over refunded bonds debt service) spanning Fiscal Years 2013 through 2030 by issuing \$87,980,000 of the UCONN 2000 Student Fee Revenue Refunding 2012 Series A Bonds. We achieved a stunning Total Net Present Value Savings of \$26,701,079 or 25.2% of the refunded principal. Working in conjunction with the Office of the State Treasurer, the University negotiated a remarkable all in True Interest Cost of 2.48 % which is the lowest interest rate for a single bond issue in the history of the program. We refunded \$106,030,000 of prior bonds including \$32,430,000 of the SO-SFR 2002 A new money bonds (all the outstanding), and \$73,600,000 of the SO-SFR Refunding 2002 A bonds (all the outstanding). The par amount of \$87,980,000 plus \$19,690,292 of the original issue premium were deposited with the Trustee bank in a \$107,670,292 irrevocable escrow fund to satisfy future debt service and call premiums on the prior issues. The bonds were issued pursuant to the Special Obligation Master Indenture and the Special Obligation Student Fee Revenue Bonds Third Supplemental Indenture, dated as of February 1, 2002.

On November 15, 2019 the University achieved debt service savings of \$2,683,550 by calling and retiring at face value the outstanding principal of \$16,745,000 of Special Obligation Student Fee Revenue 2010 Refunding bonds on their call date of November 15, 2019, from available pledged revenues. Interest payments on the outstanding debt have an average coupon of 4.6% per year. Calling and retiring the \$16,745,000 principal eliminates the \$2,683,550 of scheduled interest payments, providing a 16% return on this transaction. The University pledged revenues had been invested in the State Short Term Investment Fund which yields vary daily, but which averaged only 0.72% over the eight years prior to the call. The benefit of calling and retiring the \$16,745,000 bond principal eight years early minus the cost of earning an average of 0.72% per year results in a return of 9.66% in net present value savings of \$1,617,919 (9.66% of refunded par) in favor of retiring the bonds. Accordingly, the Board of Trustees approved the transaction on October 23, 2019, and University pledged revenues were wired to the Trustee bank's dedicated redemption account, pursuant to the indentures, sufficient to call and retire the outstanding \$16,745,000 principal at par on the day of the call. The original bonds refunded all the outstanding SO-SFR 1998-A Bonds and part of the 2002-A Bonds as further described above.

On November 15, 2022, the University achieved debt service savings of \$2,688,850 on a gross cash debt service savings basis or \$2,352,390 on a net present value basis for Fiscal Years 2023 thru 2030 by issuing \$52,515,000 of the UCONN 2000 Student Fee Revenue Refunding 2022 Series A Bonds. Working in conjunction with the Office of the State Treasurer, the University negotiated an all in True Interest Cost of 3.80 %. We refunded all outstanding SO-SFR 2012 Refunding Series A bonds, totaling \$54,795,000. The par amount of \$52,515,000 plus \$3,073,700 of the original issue premium, less costs of issuance, were deposited with the Trustee bank in a \$54,893,565 irrevocable escrow fund to satisfy future debt service and call premiums on the prior issues.

UCONN 2000 Heating Plant Upgrade Tax-Exempt Governmental Lease Purchase Agreement for the Cogeneration Facility

On December 12, 2025, the UCONN Heating Plant Governmental Lease Purchase Agreement –was fully paid off and retired.

Pursuant to Section 10a-109 of the Connecticut General Statutes, the University may issue other UCONN 2000 securities pursuant to other financing documents. The Board of Trustees authorized \$81,900,000 of UCONN 2000 debt in the form of a Heating Plant Upgrade Tax-Exempt Governmental Lease Purchase Agreement (“Heating Plant Upgrade GLPA”) secured by the University’s general obligation for the Cogeneration facility portion of the UCONN 2000 Heating Plant Upgrade project on the Storrs Campus.

This \$81,900,000 of UCONN 2000 debt was not issued under the UCONN 2000 General Obligation or Special Obligation Indentures of Trust but was entered into under certain separately negotiated documents and agreements in two parts. On December 18, 2003, the University entered a privately placed \$75,000,000 Heating Plant Upgrade GLPA with a reported nominal interest rate of 4.42% compounded monthly to finance the design and construction of a combined heat and power plant. On August 15, 2005, the University amended the agreement for an additional Heating Plant Upgrade GLPA of \$6,900,000 at a 5.09% interest rate compounded monthly (resulting in a combined interest rate of approximately 4.5%).

The Heating Plant Upgrade is a UCONN 2000 Act listed project and the funding, in addition to the \$81.9 million, has also included GO-DSC proceeds. The cogeneration facility is a linchpin of the University’s commitment to energy efficiency and generates much of the needs for electrical power, heating and cooling on the Storrs campus. Cost avoidance achieved through the construction and operation of the facility is expected to provide funds to pay the debt service.

The Heating Plant Upgrade GLPA is not rated by the credit rating agencies, however, all UCONN 2000 debt is considered in the credit rating analysis of the UCONN 2000 General Obligation and Special Obligation programs.

UCONN 2000 Heating Plant Upgrade GLPA– Refundings

Pursuant to the financing documents the University twice renegotiated the interest rate on the original financings of the Heating Plant Upgrade GLPAs and achieved a total of \$7.4 million in gross debt service savings (\$5.0 million net present value) for Connecticut taxpayers through two separate transactions.

During July 2013, the University achieved gross debt service savings of \$5.2 million by negotiating a lower interest rate amendment to the UCONN 2000 Heating Plant Upgrade- Cogeneration Facility Tax-Exempt Governmental Lease Purchase Agreement. The interest rate was lowered, effective in the

August 29, 2013, monthly payment, from 4.42% on the original \$75 million loan, and 5.09% on the original \$6.9 million loan, to 3.22% on both. The combined remaining balance of the loans was approximately \$59 million. The amendment achieved combined gross nominal debt service savings of \$5,168,392.06 million or \$3,238,326.69 (4.2%) on a net present value basis over the remaining 12 years and 5 months of the original financing.

During November 2016 the University achieved gross debt service savings of \$2.2 million by negotiating another lower interest rate amendment to the UCONN 2000 Heating Plant Upgrade-Cogeneration Facility Tax-Exempt Governmental Lease Purchase Agreement. The interest rate was lowered a full 100 basis points to 2.22% from 3.22% on the outstanding \$45.1 million balance for a debt service nominal savings of \$2,246,699.46 or present value savings of \$1,758,933.37 (3.9% as a percentage of par) over the remaining term. Monthly debt service payments which UConn pays for out of its own resources were reduced by \$20,802.76 or about \$249,633.06 a year. The new rate was effective from January 2017 to the original term of the loan ending on 12/29/2025 (approximately nine years).

UCONN 2000 Residential Life Facilities – Nathan Hale Inn Promissory Taxable Note

On December 1, 2016, the UCONN 2000 Residential Life Facilities – Nathan Hale Inn Promissory Taxable Note was fully paid off and retired.

On April 29, 2015, the Board of Trustees authorized \$5,500,000 of UCONN 2000 debt in the form of a taxable Promissory Note secured by the University's general obligation for that portion of the UCONN 2000 Residential Life Facilities project used to purchase the Nathan Hale Inn on the Storrs Campus. The Governor approved the financing on May 19, 2015.

On July 1, 2015, the University entered with Webster Bank a privately placed \$5,376,712.73 principal amount at a 6.84% interest rate known as "UCONN 2000 Residential Life Facilities (Nathan Hale Inn) Promissory Note (Taxable)" which was secured by the general obligation of the University with an approximate 18-month maturity (August 1, 2015 to December 1, 2016). The note's debt service payments are \$44,989.20 monthly with a balloon payment due on December 1, 2016. The UCONN 2000 Residential Life Facilities (Nathan Hale Inn) Promissory Note (Taxable) was issued pursuant to certain separately negotiated (by the University with Webster Bank) documents and agreements. UCONN 2000 bond counsel reviewed the process. The note was not issued pursuant to the UCONN 2000 General Obligation or Special Obligation Indentures of Trust.

UCONN 2000 DEBT SERVICE


Pursuant to Section 10a-109x of the Connecticut General Statutes, the Semiannual Report to the General Assembly is to list the payment of debt service requirements and the payment of principal and interest on the UCONN 2000 securities.

DEBT SERVICE: General Obligation Debt Service Commitment Bonds

The State General Fund pays the debt service and any arbitrage rebate due on the University's GO-DSC Bonds.

As of June 30, 2026:

- Since the program's inception in 1996, total GO-DSC debt service (which is paid by the state) amounted to \$5,936.7 million, representing \$4,023.6 million of principal and \$1,913.0 million of interest (including the Refunding Bonds but net of refunded debt).
- Of this amount, debt service of \$3,660.5 million, representing \$2,303.4 million of principal and \$1,357.1 million of interest (including capital appreciation bonds) has been paid.
- Future debt service requirements amount to \$2,276.1 million, representing \$1,720.2 million of principal and \$555.9 million of interest.
- For the Fiscal Year ending June 30, 2026, the GO-DSC bonds debt service paid was \$203.6 million, representing \$131.9 million of principal and \$71.7 million of interest.
- As of June 30, 2026, the following graph shows UCONN 2000 GO-DSC debt service by Fiscal Year including refunding issues, but net of refunded.

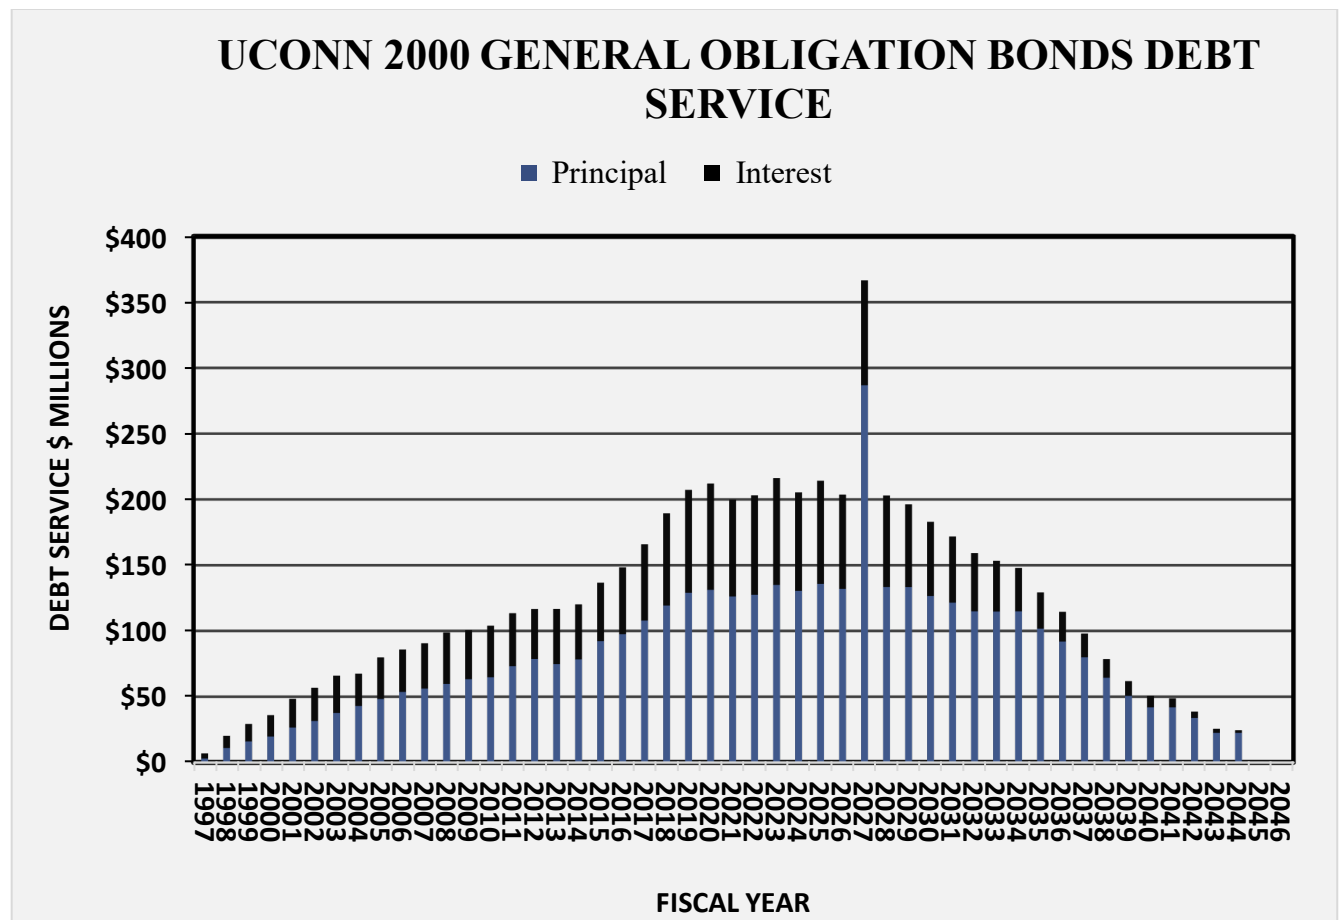

* Fiscal Year 2027 debt service reflects a short-term bond anticipation note issued on March 24, 2026, with a one-year maturity, which the University expects to refinance with long term bonds during the Spring of 2027.


DEBT SERVICE: Special Obligation Student Fee Revenue Bonds

The University is responsible for paying the debt service and any arbitrage rebate due on its Special Obligation debt. All other things equal, the Special Obligation bonds incur proportionally more interest expense because they are generally issued for terms of up to approximately thirty years compared to twenty years for the GO-DSC Bonds. The longer term of the bonds (up to 30 years) generally reflects the long-term debt cost of the assets financed by the bonds being spread more evenly over the annual benefits received by the student populations utilizing the assets.

As of June 30, 2026:

- Total UCONN 2000 SO-SFR debt service (which is paid by the University) amounted to \$815.1 million, representing \$419.9 million of principal and \$395.2 million of interest.
- Of this amount, the University had paid debt service of \$398.1 million representing \$171.1 million of principal and \$227.1 million of interest.
- Debt service remaining totals \$416.9 million comprising \$248.8 million of principal and \$168.1 million of interest.

As of June 30, 2026, the graph below shows the SO-SFR debt service paid using UConn's own funds.

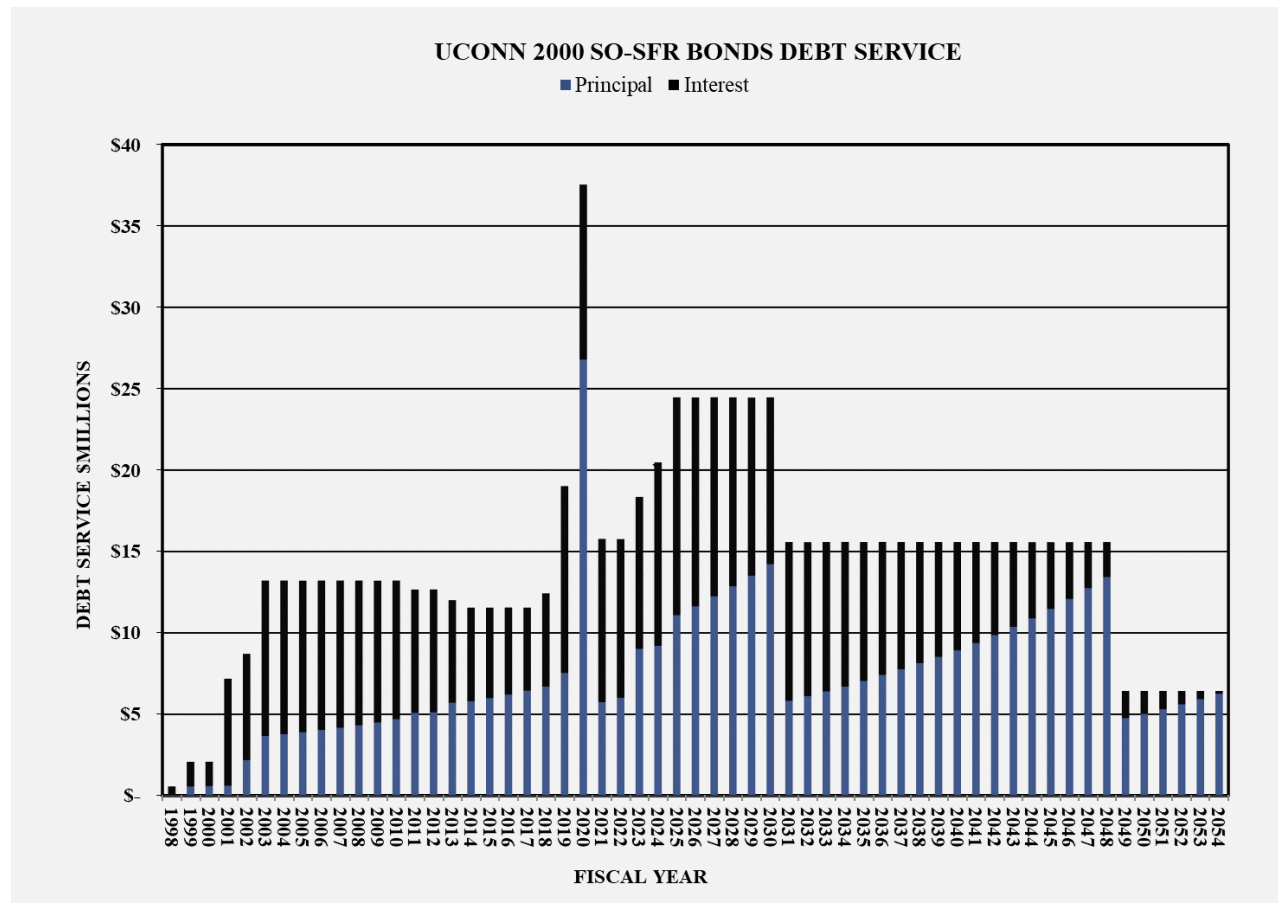

* Fiscal Year 2020 debt service includes a voluntary early call and defeasement of the SO-SFR 2010 bonds of \$16,745,000 in outstanding principal to provide future debt service savings.

DEBT SERVICE: UCONN 2000 Heating Plant Upgrade GLPA

The UConn 2000 Heating Plant Upgrade GLPA was fully paid off and retired on December 12, 2025. Over the term of the financing, the University paid total debt service of \$116.7 million representing \$81.9 million of principal and \$34.8 million of interest.

DEBT SERVICE: UCONN 2000 Residential Life Facilities (Nathan Hale Inn) Promissory Note (Taxable)

The UCONN 2000 Residential Life Facilities (Nathan Hale Inn) Promissory Note (Taxable) was retired on December 1, 2016. Over the eighteen-month term, the University paid total debt service of \$5.9 million representing \$5.4 million of principal and \$0.5 million of interest.

Investment of Debt Proceeds - Management, Investment and Earnings

The proceeds of any bond sale by the University are part of the Trust Estate established under the General Obligation Master Indenture of Trust with the Trustee Bank as security for bondholders. Consequently, the University holds all of the bond proceeds at the Trustee Bank, with the exception of the Cost of Issuance account funded by the University's GO-DSC Bonds, which may be held and invested by the State Treasurer's Office in a segregated account from which the Treasurer pays debt service to the Trustee Bank. The Special Obligation Master Indenture Trust Estate provisions includes all of the Trustee Bank Special Obligation bond proceeds received at issuance including the Costs of Issuance account, plus the periodically funded debt service fund, and the Renewal and Replacement Fund which was not funded with tax-exempt bond proceeds. The University directs the Trustee to invest and disburse these accounts.

Prior to June 1998, all UCONN 2000 GO-DSC Bond proceeds were deposited with the Office of the State Treasurer and treated like state bond proceeds, including payments made to vendors through the Office of the State Comptroller. Subsequently, the Office of the Attorney General opined that the University, and not the State, issues UCONN 2000 bonds. Accordingly, upon advice of bond counsel and in conformity with the Master Indenture of Trust, GO-DSC Bond construction fund proceeds were deposited to the Trustee Bank and disbursed as directed by the University pursuant to the Indenture. The UCONN 2000 GO-DSC Bond proceeds for costs of issuance are still treated like State bond proceeds and deposited with the Office of the State Treasurer and disbursed through the Office of the State Comptroller.

The Indentures of Trust provide that the University is authorized and directed to order each disbursement from the Construction Account held by the Trustee upon a certification filed with the Trustee bank and, in the case of the DSC bonds, the State Treasurer. The Indentures provide that such certification shall be signed by an Authorized Officer of the University and include certain disbursement information. Once the Authorized Officer certification filings are made, the University can directly disburse payments.

The investment of tax-exempt debt proceeds is heavily regulated by the Internal Revenue Service, the relevant Indentures of Trust with bondholders, Connecticut law, and other regulatory restrictions. In addition to meeting those requirements, the University's general investment policy is to balance an appropriate risk-return level, heavily weighted towards safety of assets, with

estimated cash flow needs and liquidity requirements. The University is also mindful that the rating agencies, bond buyers, and bond insurers often weigh the quality of an issuer's investment portfolio.

Bond proceeds form part of the Trust Estate established with the Trustee Bank as security for bondholders. To date, the University has directed the Trustee Bank to invest any DSC construction fund proceeds in the State Treasurer's Short Term Investment Fund ("STIF") which is "AAAm" rated by Standard and Poor's and offers daily liquidity and historically attractive risk-adjusted yields. As discussed above, the State Treasurer's Office holds and invests the University's GO-DSC funded Costs of Issuance account.

The GO-DSC Refunding, 2004, 2006, 2007, 2010, 2011, 2013, 2014, 2015, 2016, 2017, 2019, 2020, 2023 and 2026 Series A Bond proceeds, other than the costs of issuance, were deposited with the Trustee Bank to immediately redeem bonds or invest in irrevocable escrow funds, which are invested in U.S. Treasury Securities and/or U.S. Treasury State and Local Government Securities ("SLGS") and cash pursuant to the indenture and respective Escrow Agreements.

It has been the University's practice to invest all of the Special Obligation new money bond proceeds, including the debt service funds, in dedicated STIF accounts, with the exception of the 1998 Special Obligation Special Capital Reserve Fund which at times had also been invested in longer term highly rated federal agencies' fixed income Investment Obligations as defined in the Special Obligation Indenture of Trust.

The SO-SFR Refunding 2002, 2010, 2012, and 2022 Series A Bond proceeds, other than the costs of issuance and debt service accounts that were invested in STIF, were deposited with the Trustee Bank in their respective irrevocable Escrow Accounts, which were invested in SLGS, and cash pursuant to the Escrow Agreement.

The University's GO-DSC Bond proceeds investment earnings are retained and accounted for by the State Treasurer's Office and do not flow to the University or to the Trustee Bank. The University's Special Obligation bond investment earnings are part of the pledged revenues and are directly retained by the Trustee Bank to pay debt service on the bonds and may also be used to flow to other Trustee bond accounts, if necessary, pursuant to the Indenture of Trust.

Fiscal Year end June 30, 2026, UCONN 2000 SO-SFR Bond funds (not including the refunding escrows and the Renewal & Replacement Fund) investment earnings amounted to \$44,209.99 (cash basis). Additionally, for Fiscal Year end June 30, 2026, the non-bond proceeds Renewal & Replacement Fund held at the Trustee Bank (U.S. Bank Trust Company, NA) earned \$6,019,370.40 of investment earnings and were retained in that Trustee Bank account.

Investment earnings on the SO-SFR Bonds Refunding Escrow Accounts flow to their respective irrevocable escrows and are used by the Trustee Bank to meet debt service payments and redeem the defeased bonds. Similarly, investment earnings on the GO-DSC Refunding Escrow Accounts flow to each respective irrevocable escrow and are used by the Trustee Bank to meet debt service payments and redeem the defeased bonds.

On December 29, 2005, the University received \$15,847,241.65 representing the last advance of the \$81,900,000 of funds to the University under the Heating Plant Upgrade GLPA. These funds, and the related investment income, are for uses related to the Cogeneration financing and were deposited in a dedicated STIF account. During December 2006, part of the remaining proceeds, representing the initial December 18, 2003 financing, was yield restricted by investing it in a dedicated Tax-Exempt Proceeds Fund. All the Heating Plant Upgrade GLPA proceeds have been spent.

Future UCONN 2000 Debt Issuance

The University has issued the entire \$962 million of UCONN 2000 Phase I & II authorizations for the GO-DSC bonds.

UCONN 2000 Phase III, as amended, provides for an additional \$4,603,000,000 of funding with GO-DSC bonds. Of this amount, as of June 30, 2026, \$3,664,900,000 of Phase III has been authorized by the Board of Trustees and the Office of the Governor, of which \$182,900,000 is unissued. The total authorization does not include the Thirty-fourth Supplemental Indenture which is pending the Governor's approval as of June 30.

During Fiscal Year 2027, the University tentatively plans to issue new money GO-DSC Bonds, and if conditions warrant, a possible GO-DSC refunding bond issue. On June 17, 2026, UConn's Board of Trustees approved a Fiscal Year 2027 capital budget of \$475.0 million that includes \$442.1 million of GO-DSC bond funds. In future fiscal years, the University may issue additional new money GO-DSC bonds as well as refund certain GO-DSC bonds to provide debt service savings to the program, should conditions warrant.

At this time there are no Board of Trustee authorizations to issue Special Obligation bonds for UCONN 2000 projects. However, in future fiscal years, the University may issue additional Special Obligation bonds, provided that there is financial self-sufficiency capacity and aggregate pledged revenues are sufficient to meet requirements of the Special Obligation Master Indenture. Additionally, the University may refund certain SO-SFR bonds to provide debt service savings to the program, should conditions warrant.

The University could enter other types of tax-exempt or taxable financings pursuant to the UCONN 2000 Act. Market conditions and other factors could also lead to the refunding of other non-public debt in the future.

Credit Ratings

The capital markets have recognized the tangible benefits to the state's economy of meeting the infrastructure and educational goals of the program, as well as the University's success in implementing them. A good credit rating not only provides the State and the University with less expensive access to the capital markets but also supports the State's quality reputation among investors.

General Obligation Ratings

As of June 30, 2026, the University's GO-DSC Bonds were rated "AA-" by S&P Global Ratings, "Aa2" by Moody's Investors Service, and "AA" by Fitch Ratings.

On November 21, 2022, S&P Global Ratings upgraded the University's GO-DSC Bonds to "AA-" from "A+" following an upgrade of the State's General Obligation Bonds to "AA-" from "A+".

On September 9, 2025 Moody's Investor Service upgraded the University's GO-DSC Bonds to "Aa2" from "Aa3" following an upgrade of the State's General Obligation Bonds to "Aa2" from "Aa3".

On September 10, 2025, Fitch Ratings upgraded the University's GO-DSC Bonds to "AA" from "AA-".

Special Obligation Ratings

As of June 30, 2026, the University's SO-SFR Bonds were rated "A+" by S&P Global Ratings and "Aa3" by Moody's Investors Service. Fitch Ratings does not have an underlying rating for the University's SO-SFR Bonds.

On April 5, 2019, S&P Global Ratings downgraded the University's SO-SFR Bonds to "A+" from "AA-".

On October 13, 2022 Moody's Investors Service upgraded the University's SO-SFR Bonds to "Aa3" from "A1".

In addition to the underlying credit ratings, in the past the University at times would secure certain bond maturities at issuance with municipal bond insurance from FGIC, MBIA and FSA which originally provided "AAA" credit ratings. Subsequently many bond insurers experienced credit rating downgrades and other changes. At times, this has resulted in the UCONN 2000 bonds underlying credit ratings exceeding the credit ratings for certain bond insurers. Additionally, at times investors might utilize bond insurance at their own expense in the secondary market. As a result, people are advised to check with the credit rating agencies for the most recent bond ratings including those that might be so insured.

UCONN 2000 Debt Reflected on Audited Financial Statements

UCONN 2000 financings are debt obligations of the University, as the issuer, and are reflected on UConn's financial statements accordingly. For example, the SO-SFR Bonds, and the Heating Plant Upgrade GLPA and UCONN 2000 Residential Life Facilities (Nathan Hale Inn) Promissory Note (Taxable) (prior to being paid off and retired) debt are shown as liabilities on the University's financial statements and the related capital improvements are shown as assets. The University is the issuer and ultimately responsible for the GO-DSC Bonds which also fund certain assets at UConn Health, and consequently are also partially reflected on UConn Health's financial statements as further discussed below.

Phase III of the Act authorizes the University to fund projects for UConn Health with, among other sources, GO-DSC Bonds and the University has done so. Accordingly, the UCONN 2000 GO-

DSC Phase III project proceeds and any unspent debt proceeds are reflected on both UConn's and UConn Health's financial statements. As bonds are issued, the amount of the commitment for UConn Health is recorded as an offset to revenue on UConn's financial statements in the University's Other Changes in Net Position section of the Statement of Revenues, Expenses, and Changes in Net Position. A corresponding liability is recorded in due to affiliate in UConn's Statement of Net Position for the unspent portion of the bonds due to UConn Health. Correspondingly, UConn Health records that portion of UCONN 2000 bond issuance proceeds for UConn Health in the capital appropriation line in UConn Health's Statement of Revenues, Expenses, and Changes in Net Position. The corresponding receivable is recorded for the unspent portion of the bonds in the Statement on Net Position. The State's DSC for interest on the UCONN 2000 General Obligation bonds is included in Non-Operating Revenues (Expenses) section of the Statement of Revenues, Expenses, and Changes in Net Position.

UCONN 2000: Private Financial Support

For Fiscal Year 2026, the Foundation has a fundraising goal of \$145 million. As of June 30, 2026, the Foundation raised \$176 million in new gifts and commitments.

- Mr. Robert J. Skinner CLAS '93, \$15 million to support UCONN Athletics
- Mr. Mark L. Goldenson, \$11 million to support the College of Liberal Arts and Sciences through the establishment of a Center in Actuarial Science
- Mr. John Y. Kim BUS '86 BUS '16, \$10 million to support the University of Connecticut Health Center
- Mrs. Elisabeth C. DeLuca, NURS '69, \$9.7 million to support the School of Nursing and the Waterbury Campus
- Mr. Douglas G. Elliot, BUS 1982, BUS (HON) 2017, \$5 Million to support UCONN Athletics programs and UCONN students
- Mr. Christopher T. Fraser BUS '80 CLAS '80 and Mrs. Karen C. Fraser, \$4.2 million to support UCONN Football program and students
- Robert W. Sperry, Jr., \$3.8 million for programmatic support of UCONN programs

UCONN 2000 in CYBERSPACE

Information about UCONN 2000 is available on the World Wide Web at:

<https://bpir.uconn.edu/home/capital-budget/capital-reports-and-presentations/uconn2000reports/>

The website contains all previous legislative updates to the Governor and the General Assembly (Progress Reports), the four-year Progress Report, the original UCONN 2000 proposal and UCONN 2000 project updates.

University of Connecticut
FY27 Capital Budget Spending Plan
Approved Projects by Statutory Named Lines & by Program*

UCONN 2000 Bond Funded Projects by Named Lines	Statutory	Total	By Program		
			Academic/ Research	Deferred Maint.	Other
Academic and Research Facilities		\$28.5			
Gant Repairs & Renovations	23.5		23.5		
Academic Building	5.0		5.0		
Deferred Maintenance		152.5			
Building Renewal Program-Interior and Exterior Repairs, Code Compliance, and Abatement	5.0			5.0	
Campus Roadway Rehabilitation and Resurfacing Program - Horsebarn Hill and Others	5.0			5.0	
Environmental Remediation and Underground Tank Relocations	3.0			3.0	
Field House and Gampel Improvements	76.5				76.5
HVAC Infrastructure Renewal Program- Equipment, Controls, Chillers & Humidity Control Improvements	3.0			3.0	
Northeast Campus Infrastructure Improvements	3.0			3.0	
NW Quad: University 2nd Electrical Feed	3.0			3.0	
Pedestrian Access and Safety Improvement Program-Sidewalk, Ramp, Stair and Entrance Repairs	5.0			5.0	
Programmatic Renovations	33.0		33.0		
Strategic Renovations for Lease Exits and Occupancy Consolidation	5.0			5.0	
Surface & Garage Parking	6.0				6.0
Contingency	5.0		5.0		
Equipment		54.1			
Information Technology & University Safety	15.7				15.7
Faculty Start-up	38.4		38.4		
UCH DM		90.0			
UCH Deferred Maintenance	90.0			90.0	
UCH Equipment		41.0			
UCH Equipment, Library Collections and Telecommunications	6.0			6.0	
UCH System Telecom Infrastructure Upgrades, Improvements	35.0				35.0
UCH Joint Venture		76.0			
Joint Venture - Deferred Maintenance Finance Corp	16.0			16.0	
Joint Venture - Information Technology/Equipment Finance Corp	50.0			25.0	25.0
Joint Venture - Working Capital (or Information Technology/Equipment)	10.0				10.0
Total UCONN 2000 Bond Funded Projects		\$442.1	\$104.9	\$169.0	\$168.2
Other Funded Projects (University, Gifts)					
Facilities Repairs & Improvements (University)		11.1		11.1	
Residential Refresh Program (University)		20.0		10.0	10.0
Energy Program & Solar Array (Gifts)		1.8			1.8
Total Other Funded Projects		\$32.9	\$0.0	\$21.1	\$11.8
Grand Total FY27 Capital Budget		\$475.0	\$104.9	\$190.1	\$180.0

*Projects less than \$500,000 are approved by UConn administrative committee. Projects costing \$500,000 or more are submitted for Board action on a project by project basis.

UCONN 2000 Bonds
State General Obligation Bond Phasing Plan & Actuals by Statutory Named Line

Project	Authorization as of 5.31.26*				Actuals as of 5.31.26		
	FY96-FY25	FY26	FY27-31	Total Phases I, II, III	Expenditures	Encumbrances	Available**
Academic and Research Facilities	\$435,704,438	\$54,000,000	\$284,500,000	\$774,204,438	\$393,951,660	\$78,849,570	\$16,903,208
Agricultural Biotechnology Facility & Completion	12,400,000			12,400,000	12,400,000		
Alumni Quadrant Renovations	11,183,624			11,183,624	11,183,624		
Arjona and Monteith (new classroom buildings)	128,219,871			128,219,871	128,219,871		
Avery Point Campus Undergraduate & Library Building	10,461,246			10,461,246	10,461,246		
Avery Point Marine Science Research Center - Phase I & II	37,254,246			37,254,246	37,254,246		
Avery Point Renovation	13,203,165			13,203,165	13,203,165		
Beach Hall Renovations	5,146,688			5,146,688	5,146,688		
Benton State Art Museum Addition	3,603,509			3,603,509	3,603,509		
Biobehavioral Complex Replacement	3,495,807			3,495,807	3,495,807		
Bishop Renovation	2,480,141			2,480,141	2,480,141		
Business School Renovation - Phase II	7,958,470			7,958,470	7,958,470		
Central Warehouse New	6,933,752			6,933,752	6,933,752		
Chemistry Building	53,062,000			53,062,000	53,062,000		
Deferred Maintenance-Storrs & Regionals	1,154,177,619	69,500,000	126,450,000	1,350,127,619	1,016,095,019	86,018,963	121,563,637
East Campus North Renovations	7,382,605			7,382,605	7,382,605		
Engineering Building	92,579,390			92,579,390	92,579,390		
Equipment, Library Collections & Telecommunications	381,253,656	4,500,000	35,050,000	420,803,656	366,566,224	2,417,521	16,769,911
Family Studies (DRM) Renovation	2,868,306			2,868,306	2,868,306		
Farm Buildings Repairs/Replacement	6,408,304			6,408,304	6,408,304		
Fine Arts Phase II	38,792,721			38,792,721	38,792,721		
Floriculture Greenhouse	6,691,799			6,691,799	6,691,799		
Gant Plaza Deck	7,287,174			7,287,174	7,287,174		
Gant Building Renovations	12,455,770			12,455,770	12,455,770		
Gentry Renovation & Completion	19,292,806			19,292,806	19,292,806		
Grad Dorm Renovations	2,928,228			2,928,228	2,928,228		
Hartford Relocation Acquisition/Renovation	139,027,625			139,027,625	139,027,625		
Heating Plant Upgrade	21,846,724			21,846,724	21,846,724		
Hilltop Dormitory Renovations	8,176,529			8,176,529	8,176,529		
Ice Rink Enclosure	3,280,000			3,280,000	3,280,000		
International House Conversion (Natural History Museum)	886,134			886,134	886,134		
Intramural, Recreational & Intercollegiate Facilities	31,009,921			31,009,921	31,009,921		
Jorgensen Renovation	3,899,129			3,899,129	3,899,129		
Koons Hall Renovation/Addition	1,461,146			1,461,146	1,461,146		
Lakeside Renovation	3,800,000			3,800,000	3,800,000		
Law School Renovations/Improvements	16,660,677			16,660,677	16,660,677		
Litchfield Agricultural Center - Phase I	1,000,000			1,000,000	1,000,000		
Manchester Hall Renovation	772,577			772,577	772,577		
Mansfield Apartments Renovation	2,071,000			2,071,000	2,071,000		
Mansfield Training School Improvements	6,500,000			6,500,000	6,386,221	-	113,779
Monteith Renovation	444,348			444,348	444,348		
Music Drama Addition	7,400,000			7,400,000	7,400,000		
Natural History Museum Completion	500,000			500,000	500,000		
North Campus Renovation	10,996,050			10,996,050	10,996,050		
North Hillside Road Completion	6,700,000			6,700,000	6,700,000		
North Superblock Site & Utilities	7,668,000			7,668,000	7,668,000		
Northwest Quadrant Renovation - Phase I & II	32,001,000			32,001,000	32,001,000		
Old Central Warehouse Renovation	126,000			126,000	126,000		
Parking Garage North	9,658,000			9,658,000	9,658,000		
Parking Garage #3	75,214			75,214	75,214		
Pedestrian Walkways (Fairfield Road Pedestrian Mall)	6,074,000			6,074,000	6,074,000		
Psychology Building Renovation/Addition	24,337,399			24,337,399	24,337,399		
Residential Life Facilities	248,538,476			248,538,476	247,294,659	708,887	534,930
School of Business	25,652,366			25,652,366	25,652,366		
School of Pharmacy/Biology	94,609,000			94,609,000	94,553,295	-	55,705
Shippee/Buckley Renovations	6,920,000			6,920,000	6,920,000		
South Campus Complex	12,251,000			12,251,000	12,251,000		
Stamford Downtown Relocation - Phase I	55,781,472			55,781,472	55,781,472		
Stamford Campus Improvements/Housing	1,500,870			1,500,870	1,500,870		
Storrs Hall Addition	14,664,091			14,664,091	14,664,091		
Student Union Addition	57,622,633			57,622,633	57,622,633		
Support Facility (Architectural & Engineering Services)	16,583			16,583	16,583		
Technology Quadrant - Phase IA	39,993,000			39,993,000	39,993,000		
Technology Quadrant-Phase II	34,120,000			34,120,000	34,120,000		
Torrey Life Science Renovation & Completion	1,781,482			1,781,482	1,781,482		
Torrington Campus Improvements	369,156			369,156	369,156		

UCONN 2000 Bonds
State General Obligation Bond Phasing Plan & Actuals by Statutory Named Line

Project	Authorization as of 5.31.26*				Actuals as of 5.31.26		
	FY96-FY25	FY26	FY27-31	Total Phases I, II, III	Expenditures	Encumbrances	Available**
Towers Renovation	17,950,243			17,950,243	17,950,243		
Underground Steam & Water Upgrade - Phase I & II	12,000,000			12,000,000	12,000,000		
Waring Building Conversion	11,452,000			11,452,000	11,452,000		
Waterbury Property Purchase	200,000			200,000	200,000		
Waterbury Downtown Campus	1,608,764			1,608,764	1,608,764		
West Campus Renovations	519,507			519,507	519,507		
West Hartford Campus Renovations/Improvements	6,774,305			6,774,305	6,774,305		
White Building Renovation	2,427,269			2,427,269	2,427,269		
Wilbur Cross Building Renovation	19,999,571			19,999,571	19,999,571		
Young Building Renovation/Addition	23,651,403			23,651,403	23,651,403		
SUBTOTAL FOR STORRS & REGIONAL CAMPUS	\$3,500,000,000	\$128,000,000	\$446,000,000	\$4,074,000,000	\$3,304,063,888	\$167,994,941	\$155,941,170
CLAC Renovation Biosafety Level 3 Lab	15,901,466			15,901,466	15,901,466		
Deferred Maintenance-UCH	76,959,697			76,959,697	71,256,474	-	5,703,223
Dental School Renovation	3,525,000			3,525,000	3,525,000		
Equipment, Library Collections & Telecom-UCH	116,429,390			116,429,390	116,429,390		
Library/Student Computer Center Renovation	1,266,460			1,266,460	1,266,460		
Main Building Renovation	117,484,316			117,484,316	117,484,316		
Medical School Academic Building Renovation	39,578,232			39,578,232	39,578,232		
Planning & Design Costs	25,000,000			25,000,000	25,000,000		
Research Tower	67,992,229			67,992,229	67,992,229		
Joint Venture Initiative-UCH	-	148,000,000	242,000,000	390,000,000	9,347,078	-	138,652,922
Support Building Addition/Renovation	100,000			100,000	100,000		
UCH New Construction and Renovation	386,663,210			386,663,210	386,663,210		
SUBTOTAL FOR HEALTH CENTER	\$850,900,000	\$148,000,000	\$242,000,000	\$1,240,900,000	\$854,543,855	\$0	\$144,356,145
GRAND TOTAL	\$4,350,900,000	\$276,000,000	\$688,000,000	\$5,314,900,000	\$4,158,607,743	\$167,994,941	\$300,297,315

* UCONN 2000 Bond Authorization is separate from and does not agree to UCONN 2000 Bonds Sold, which totals \$4,444,000,000 as of the reported date. This results in a difference of \$182,900,000 between total UCONN 2000 Bonds authorized and total UCONN 2000 Bonds sold.

** The available balance is calculated as FY96-FY26 UCONN 2000 Bond Authorization, less expenditures and encumbrances. As stated above, the bond authorization is separate from bonds sold. The total available balance from bonds sold would be \$182,900,000 less, or \$117,397,315.

EXHIBIT C

POLICIES: SELECTION AND ACQUISITION OF PROFESSIONAL SERVICES

Section 10a-109d (5) of the Connecticut General Statutes authorizes the University to contract with professionals to plan, design and supervise UCONN 2000 projects and other capital projects.

1. The Vice President of Finance and Chief Financial Officer has the responsibility for the administration of these policies. Authority for their implementation may be delegated to appropriate operating departments and/or individuals.
2. A selection committee shall be appointed to select professional services for each project in accordance with university policies and procedures.
3. The selection committee shall develop the rating and evaluation criteria.
4. The contract shall be negotiated in consultation with the Vice President for Facility Services & University Planning or with the Vice President of Facilities Development & Operations for the Health Center.
5. Changes in scope that affect the cost of the project must be approved by the Vice President of Finance and Chief Financial Officer, or as delegated to appropriate operating departments and/or individuals.

EXHIBIT D

POLICIES: PRE-QUALIFICATION AND SELECTION OF CONTRACTORS


Section 10a-109n (c) (2) of the Connecticut General Statutes authorizes the University to contract with construction firms for the building of UCONN 2000 projects and other capital projects.

1. The Vice President of Finance and Chief Financial Officer has the responsibility for the administration of these policies. Implementing authority may be delegated to appropriate operating departments.
2. Pre-qualification shall be required of all bidders for projects over \$100,000.
3. Objective, written criteria for pre-qualification of firms shall be developed.
4. A list of pre-qualified contractors shall be developed on a project basis. Firms will be evaluated on written criteria, including but not limited to: (1) the firm's previous experience with similar projects, (2) the firm's financial ability to complete the project, (3) the firm's ability to post surety bonds, (4) evaluation of the firm's integrity, (5) a determination that the firm has no conflict of interest in connection with the project, (6) technical ability, (7) managerial ability and (8) whether a contractor or one of their subcontractors on one of their previous projects has been in compliance with the provisions of Part III of Chapter 557 and Chapter 558 during the previous five calendar years.
5. Pre-qualified firms shall be invited to bid upon a specific contract. Contracts shall be awarded to the lowest responsible bidder who conforms to the University's standards for the project.
6. If it is in the best interest of the University and the State of Connecticut, all bids may be rejected, and the contracting process reopened.
7. The University may negotiate with any pre-qualified contractor that is currently under contract for incorporation work under exigent circumstance. This new work need not be related to the original contract. The new work shall be of a similar nature as the basic contract.
8. Exigent circumstances include work necessary to:
 - a. Prevent loss of grant income or other revenue
 - b. Produce additional revenue or grant income
 - c. Ensure renovations are complete for new faculty and staff members
 - d. Provide for safety and health of the University Community
 - e. Comply with any Federal or State laws or regulations
 - f. Ensure timely and orderly completion of UCONN 2000 or 21st Century UConn Projects.

9. The Vice President of Finance and Chief Financial Officer shall approve use of the exigency provision for an individual job based upon a written recommendation from Vice President for Facility Services & University Planning or the Vice President of Facilities Development & Operations for the Health Center.
10. The negotiations may be conducted with any contractor or contractors currently performing one of the following types of contracts: lump sum, design build or construction manager at risk.
11. Vice President for Facility Services & University Planning or with the Vice President of Facilities Development & Operations as designee for the Health Center will prepare a price negotiations memorandum detailing the basis for the award.
12. The Vice President of Finance and Chief Financial Officer shall also stipulate whether the added work shall be incorporated into the contract by change order or be consummated as a new contract.


Investment Growth

In Millions of Dollars

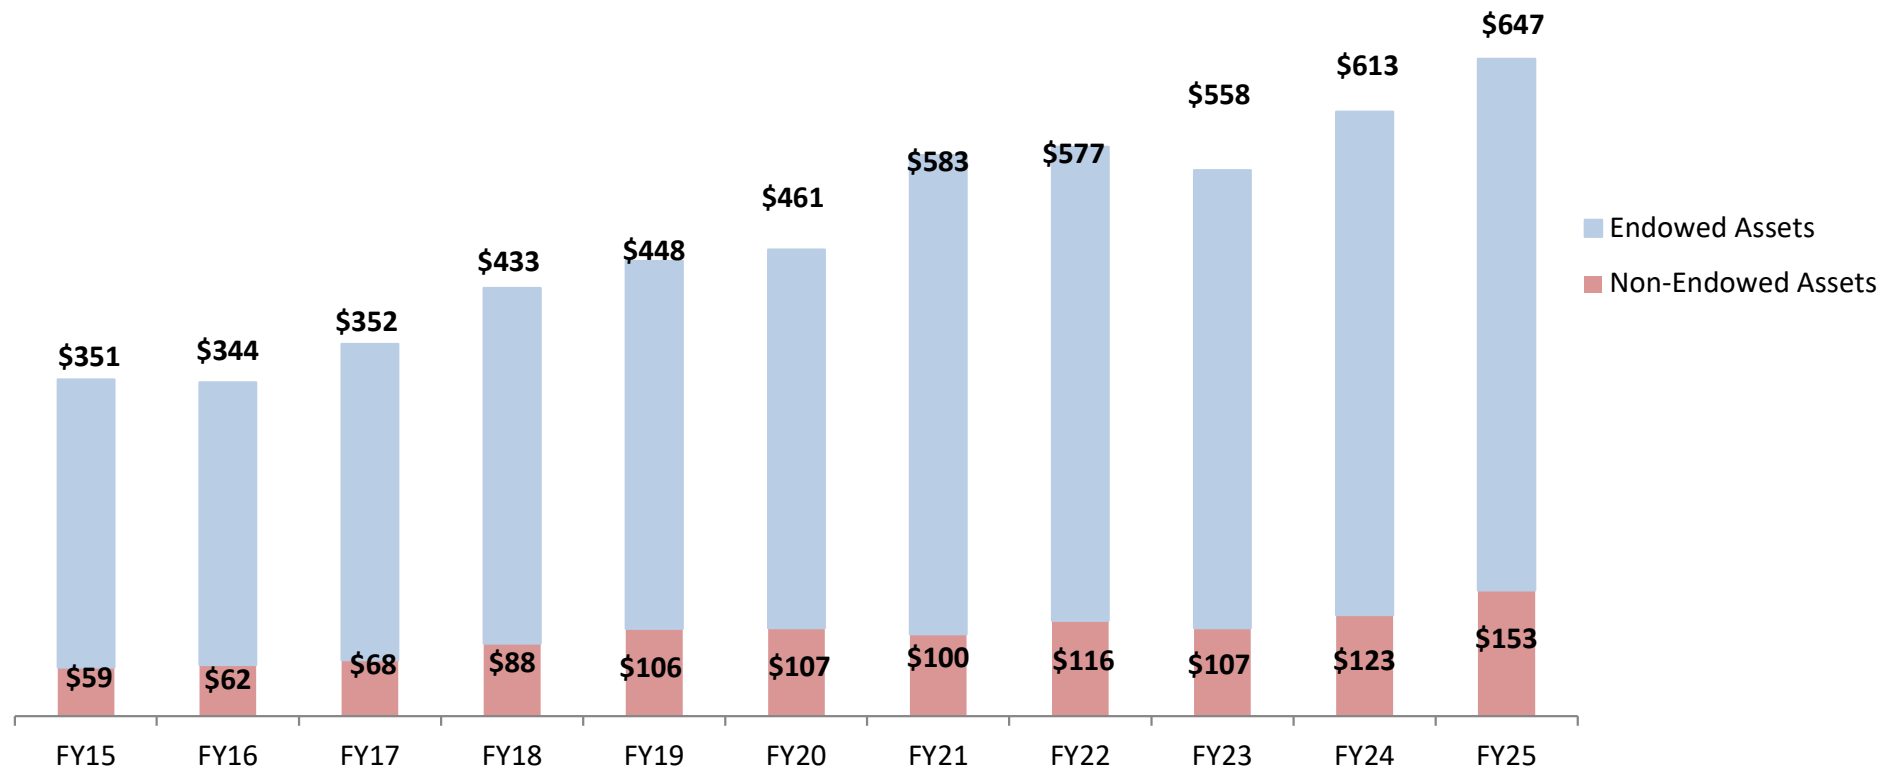


Total Endowment Gift Receipts for the University of Connecticut

In Millions of Dollars

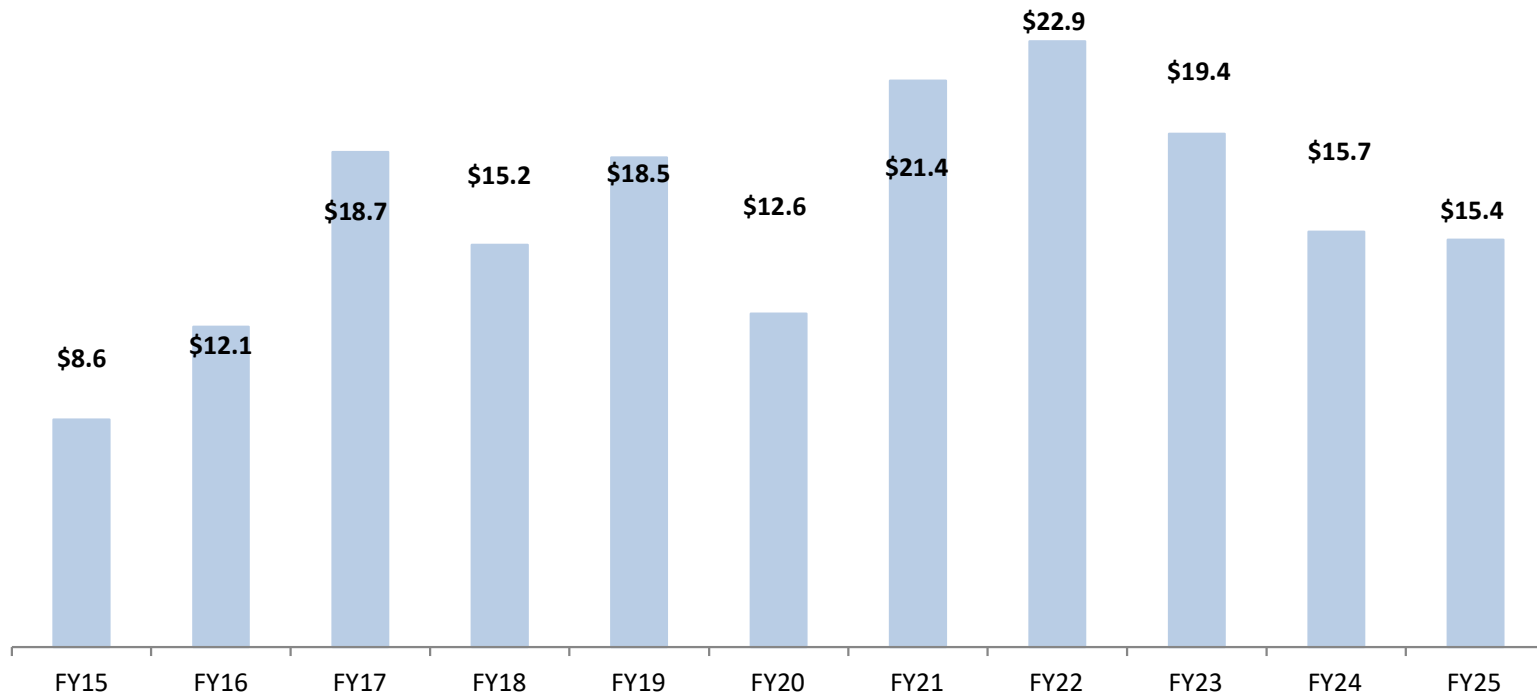

Total Gift Receipts for the University of Connecticut

In Millions of Dollars

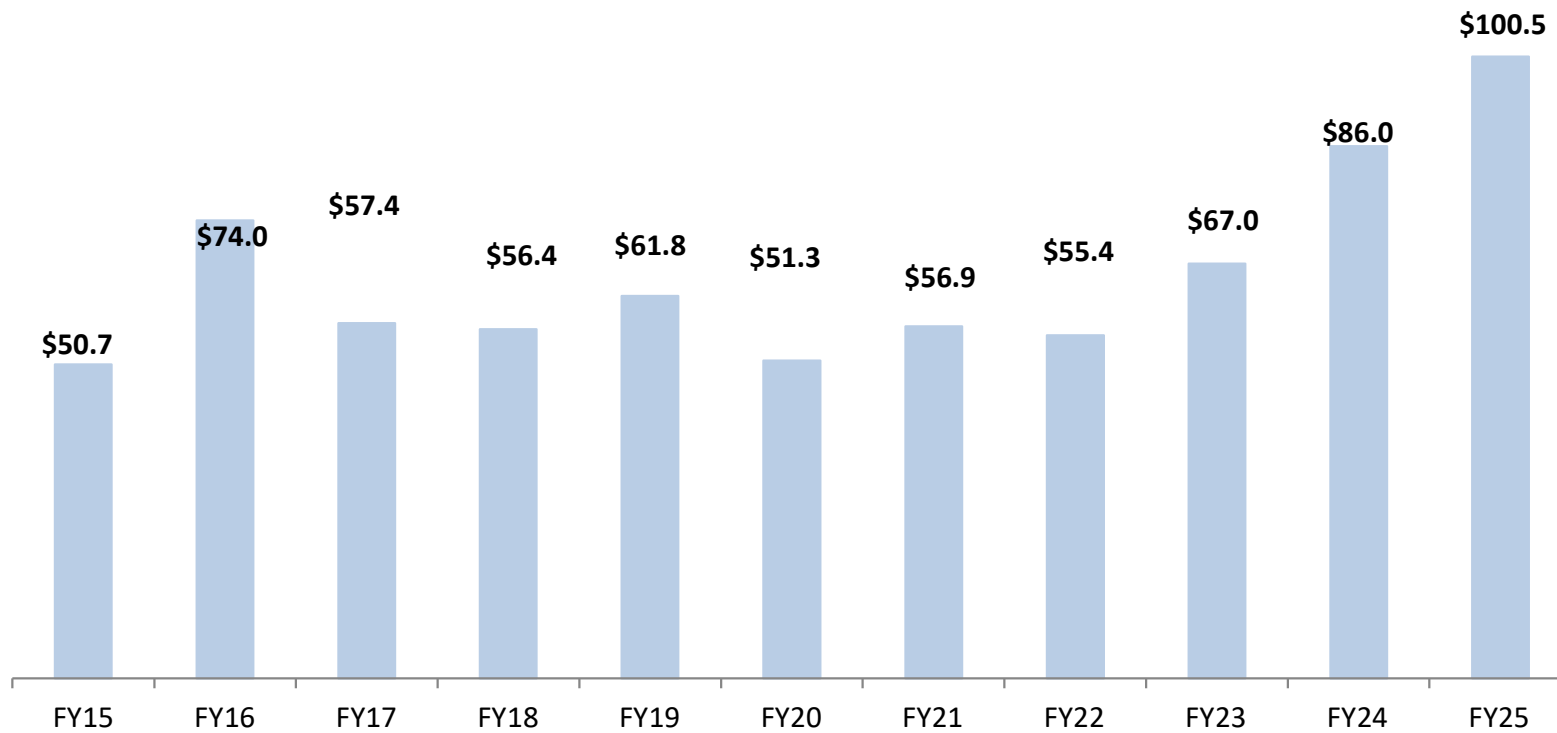

ATTACHMENT A
Alphabetical Listing of Contractors and Subcontractors
January 1,2026 thru July 1, 2026

Company Name	Address 1	Town	State	Zip Code
A-1 Services Inc	127 Colony Street	Meriden	CT	06451
A & A Drywall and Acoustics Inc	360 New Haven Ave	Milford	CT	06460
Advanced Sheetmetal Associates LLC	52 Industrial Park Access Road	Middlefield	CT	06455
AEN Asphalt INC	45 Lebanon Road	Franklin	CT	06254
All Seasons Landscaping Inc	120 Commerce Cort	Cheshire	CT	06410
Amenta Emma Architects PC	242 Trumbull Street	Hartford	CT	06103
A-Quick Pick Crane Service Co Inc	205 Water Street	Derby	CT	06418
Arc Electric LLC	38 Eagle Drive	Shelton	CT	06484
Automatic Door DR Inc	250 Main Street	Wallingford	CT	06492
Barall & Konover Floors Inc	714 Blue Hills Avenue	Hartford	CT	06112
Barber Fireshop Systems LLC	175 Englewood Drive	Orange	CT	06477
Beacon Light & Supply Co	422 North Main Street	Manchester	CT	06042
Blackwater Services Group LLC	117 Great Hill Road	Naugatuck	CT	06770
C & A Distributors Inc	105 Pane Road	Newington	CT	06111
C & H Electric Inc	1999 South Main Street	Waterbury	CT	06706
Central Conn Acoustics Inc	105 North Cherry Street	Wallingford	CT	06492
Commercial Roofing & Contracting Inc	340 Kennedy Drive, PO Box 647	Putnam	CT	06260
Consolidated Electric Inc	100 Wheeler Street	New Haven	CT	06512
DeAngelo Contracting Inc	212 Nartin Road	Bristol	CT	06010
Dicin Electric Co Inc	156 Cross Road	Waterford	CT	06385
Division 5 LLC	99 Cooper Lane	Stafford Springs	CT	06076
Eagle Environmental Inc	8 South Main Street	Terryville	CT	06786
Eastern Mechanical Services Inc	97 Willenbrock Road	Oxford	CT	06478
EF & G Construction Inc	15 Robert Jackson Way	Plainville	CT	06062
Electrical Services Inc	37 Townsend Avenue	New Haven	CT	06512
Ernest Peterson Inc	1830 Broad Street	Hartford	CT	06114
Friar Architecture Inc	21 Talcott Notch Road	Farmington	CT	06032
Ford & Ulrich Inc	459 Washington Avenue	North Haven	CT	06473
Fotaleza Concrete LLC	504 Forest Road	Northford	CT	06472
Fire Rated LLC	17A Canal Street	Terryville	CT	06786
G Donovan Associates Inc	627 Route 32	North Franklin	CT	06254
General Welding & Fabrication Inc	977 Echo Lake Road	Watertown	CT	06795
Genovesi Construction LLC	97 Gerber Drive	Tolland	CT	06084
HHS Mechanical Contractors	80 Colonial Road	Manchester	CT	06042
Industrial Electric & Construction LLC	50 Robert Jackson Way	Plainville	CT	06062
JE Shea Electric Inc	45 East Summer Street	Plantsville	CT	06479
JHS Restoration Inc	170 Stron Road	South Windsor	CT	06074
JLY Enterprises Inc	990 State Street	New Haven	CT	06511
John Boyle Company	PO Box 397	Nw Britain	CT	06051
K & L Welding	2025 Main Street	Hartford	CT	06120
L & P Gate Company Inc	83 Meadow Street	Hartford	CT	06114
L&R Mechanical Services LLC	461 Broad Street	Bristol	CT	06010
LePine & Family Electric LLC	436 Lisbon Road	Canterbury	CT	06331
Linda J Wray	315 Butlertown Road	Oakdale	CT	06370
M. Frank Higgins & Co Incorporated	780 North Mountain Rd	Berlin	CT	06111
MacKenzie Painting Company	55 Moffitt Street	Startford	CT	06615
Maier Design Group LLC	34 Sequassen Street	Hartford	CT	06106
Mather Corporation	21 West Corporation Town Road	Bloomfield	CT	06002

Company Name	Address 1	Town	State	Zip Code
Mattern Construction Inc	26 Bushnell Hollow Rd Ste M	Baltic	CT	06330
Mazzotta Rentals Inc	77 Boston Road	Middletown	CT	06457
National Sign Corp	780 Four Rod Road	Berlin	CT	06037
NET Services LLC	77 Industrial Park Road	Vernon	CT	06066
Northeast Flooring and Kitchens LLC	17 Kennedy Drive	Putman	CT	06260
Northeastern Engineering and Contracting Company LLC	115 Daleville School Road	Willington	CT	06279
Nosal Builders Inc	85 Fieldstone Court Unit 1	Cheshire	CT	06410
Old Colony Construction LLC	10 Bluff Ave Unit 121	Clinton	CT	06413
Opticom Inc	217 Pickering Street	Portland	CT	06513
Orissa LLC	45 Andover Drive	Rocky Hill	CT	06067
Park Roway Inc	51 Route 32	Quaker Hill	CT	06375
Perfectly Plumb LLC	215 Pickerel Lake Road	Colchester	CT	06415
Plumbing Solutions LLC	27 Fulton Street	New Haven	CT	06513
Prime Electric LLC	33 Wisconsin Ave	Norwich	CT	06360
Quisenberry Arcari Malik LLC	195 Scott Swamp Road	Farmington	CT	06032
R&B Ceramic Tile & Floor Covering Inc	10 Pickett Ave	Wallingford	CT	06492
RN Pro Painting LLC	197 Edge Wood Road	Kensington	CT	06037
Reynolds Welding & Fabrication LLC	148 Addison Road	Windsor	CT	06095
Ruotolo Mechanical Inc	29 Printers Lane	New Haven	CT	06519
Safety Solution Consultants Inc	9 School Street	East Granby	CT	06026
Sarazin General Contractors Inc	6 Commerce Drive	North	CT	06256
Scholar Painting LLC	2 Klarides Village Drive	Seymour	CT	06483
Sign Pro Inc	60 Westfield Drive	Plainville	CT	06479
Sil/Carr Corporation	34 Newberry Road	East Windsor	CT	06088
Silver Petrucelli & Associates Inc	3190 Whitney Ave	Hamden	CT	06518
SK Mechanical LLC	266 Center Street	Manchester	CT	06040
SMI Demolition Inc	266 Center Street	Manchester	CT	06040
Stonehedge Landscaping Company Inc	1616 Willard Ave	Newington	CT	06111
TC Lawncare LLC	101 Crouch Road	Amston	CT	06231
T&T Electrical Contractor's Inc	420 Windsor Street	Hartford	CT	06120
Test-Con Incorporated	16 East Franklin Street	Danbury	CT	06810
Tri State Materials Testing Lab LLC	41 Breezy Corners Rd	Portland	CT	06480

PREVAILING WAGE COMPLIANCE REPORT

The attachments referred to below cover the reporting period from January 1, 2025 thru June 30, 2025 and are issued pursuant to the requirements of subsection (f) of section (7) of Public Act 02-3, an Act Concerning 21st Century UCONN, by providing the following information:

(1) The names and addresses of contractors and subcontractors performing repair, addition, alteration and new construction on the university's campuses in the previous six months.

Attachment A provides the listing in alphabetical order. This is being filed in conjunction with the July 2025 Report Number Sixty to provide a consolidated report for UCONN 2000 activities. There is no sub-grouping of contractors or subcontractors as the nature of their business makes each interchangeable with the other as business opportunities become available.

Attachment B is based on information from the State of Connecticut Department of Labor, Wage and Workplace Standards Division, Contract Compliance Unit and represents a combined sharing of information by the University of Connecticut and the Department of Labor. No report is made from the Department of Labor, for this reporting period.

Attachment C is the Debarment list issued by the Department of Labor.

September 23, 2025

State of Connecticut Debarment List Pursuant to Section 31-53a(a)

No contract shall be awarded to any person or firms appearing on this list or to any firm, corporation, partnership, or association in which such persons or firms have an interest until the expiration date listed has elapsed.

Please be informed that the following persons or firms have been debarred in accordance with Section 31-53a of the Connecticut General Statutes, as amended:

DEBARMENT LIST	
<u>Name of Person or Firm</u>	<u>Expiration Date</u>
-Canterbury Communications, Canterbury Marion T. Mershon, an individual	Indefinite Indefinite
-Elite Roofing, Cheshire Sam Stevens, an individual	Indefinite Indefinite
-Gatollari Enterprises Inc., Rochelle Park, NJ Robert Gatollari, an individual	Indefinite Indefinite
-Greenland Enterprises Inc., Wayne, NJ Oneil Mendez, an individual Raymond Blum-Romero, an individual	Indefinite Indefinite Indefinite
-Jarosz Welding Company Inc., Hartford	Indefinite
-SCD Services, LLC, Somers Philip Snow, an individual	Indefinite Indefinite
-Seakco Construction, Stamford Robert Evans, an individual	Indefinite Indefinite
-Sun Ray Electric, Prospect Reinaldo DeSousa, an individual	Indefinite Indefinite

Any inquiries regarding this list should be directed to the Wage and Workplace Standards Division at (860)263-6790.



Danté Bartolomeo
Labor Commissioner

Board of Trustees
University of Connecticut

The Honorable Ned Lamont
(Governor of the State of Connecticut)
(President ex-officio)

Daniel D. Toscano
(Chairman of the Board)

John P. Driscoll
(Chair, UConn Health Board of Directors)
(Member ex-officio)

Charlene M. Russell-Tucker
(Commissioner of Education)
(Member ex-officio)

Bryan P. Hurlburt
(Commissioner of Agriculture)
(Member ex-officio)

Daniel H. O'Keefe
(Commissioner, Department of Economic & Community Development)
(Member ex-officio)

Trisha M. Bailey

Denis J. Nayden

George A. Barrios

Brian K. Pollard

Andy F. Bessette

Thomas D. Ritter

Mark L. Boxer

Philip E. Rubin

Charles F. Bunnell

Fabio R. Saccomanno

Shari G. Cantor

Richard I. Vogel

Andrea Dennis-LaVigne

Diane W. Whitney

Nina Lemash

